

Present Status of

**RSETIs**


**BANK WISE**

at a Glance

as on **28.02.2018**

# AGVB – 3

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
0	0	2	0	1	0

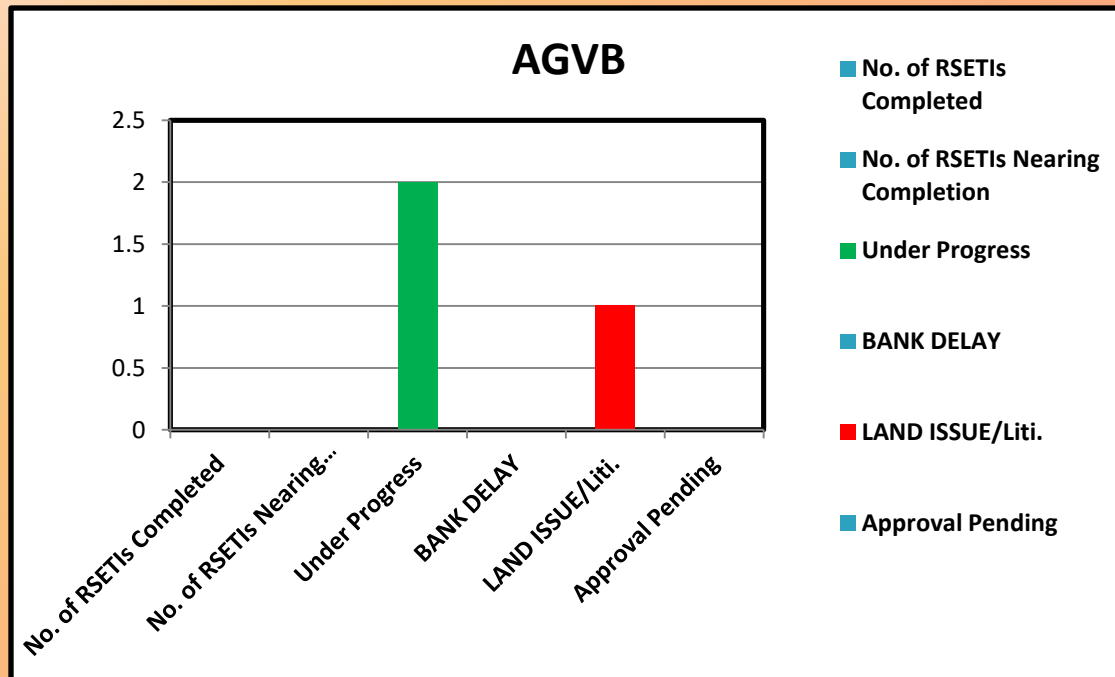


# ASSAM GRAMIN VIKAS BANK (AGVB)

S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>LITIGATION</b>				
1	Bongaigoan	Assam	50.00000	CONSTRUCTION AFFECTED DUE TO OBJECTION FROM <b>FISHERIES DEPARTMENT</b> , GoA.
<b>UNDER PROGRESS</b>				
2	Jorhat	Assam	50.00000	LIKELY TO BE COMPLETE on <b>31-3-2018</b>
3	Sonitpur	Assam	50.00000	LIKELY TO BE COMPLETE on <b>31-3-2018</b>

## ALLAHABAD BANK - 17

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>1</b>	<b>7</b>	<b>7</b>	<b>1</b>	<b>1</b>	<b>0</b>

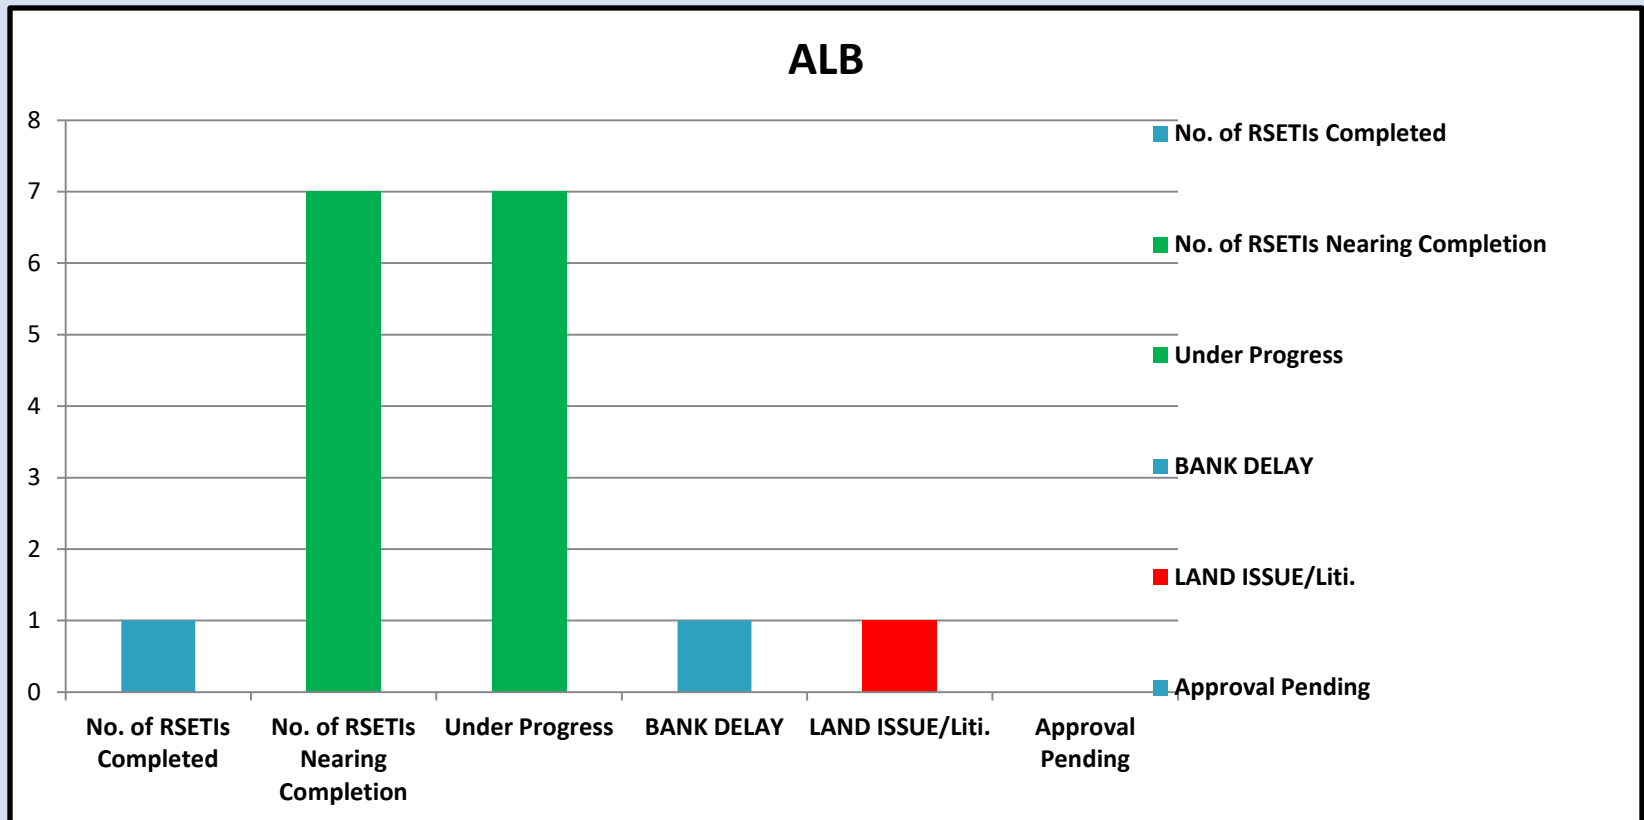

# ALLAHABAD BANK

S.NO	RSETI	STATE	FUNDS Released	REMARKS
<b>NEARING COMPLETION</b>				
1	Chitrakoot	U.P.	99.24000	<b>Roof casting</b> of both GF & FF, Brick works done. Plastering going on
2	Gonda	U.P.	50.00000	Plastering work completed, <b>Plumbing</b> works to be done
3	Dumka	Jharkhand	50.00000	Centering works going on for roof casting
4	L-Kheri	U.P.	98.17000	Likely to be completed on <b>31.1.2018</b>
5	Mahoba	U.P.	98.57000	<b>Plastering work</b> is under progress
6	Hamirpur	U.P.	99.12000	Plastering work completed, <b>Plumbing</b> works to be done
7	Sitapur	U.P.	98.16469	ROOF CASTING OF BOTH FLOOR CMPLTD, likely to be on <b>28.2.2018</b>
<b>UNDER PROGRESS</b>				
1	Godda	Jharkhand	50.00000	<b>Plinth work</b> Completed, Pillars being raised.
2	Hazaribagh	Jharkhand	50.00000	<b>Columns built</b> up to plinth level, held up by the contractor for raising plinth and again started after clarification from HO Premises.
3	Satna	Madhya Pradesh	50.00000	<b>ROOF CASTING</b> OF BOTH FLOOR CMPLETED, Brick works up to lintel level completed

## ALLAHABAD BANK


**Cont.**

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	Jalaun(Orai	U.P.	50.00000	Brick work of ground floor in progress likely to be complete on <b>April 2018</b>
2	Mirzapur	U.P.	50.00000	<b>Plinth Level</b> Completed, Pillars raised up to roof level
3	Shrawasti	U.P.	50.00000	Upto <b>Lintel level</b> pillars raised
4	Sonbhadra	U.P.	50.00000	<b>Plinth Level</b> Completed, Pillars are being raised
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Bolpur/Bhirbhum	West Bengal	10.00000	Physical possession could not be taken due to protest, <b>separate land to be allotted</b>
2	Banda	U.P.	50.00000	DRDA is not allowing for construction, <b>Alternate land</b> will be provided by the dist. authorities
<b>BANK DELAY</b>				
1	Debra/west medinapur	West Bengal	10.00000	Architect Appointed, <b>Plan to be submitted for the approval</b>
2	Balrampur	U.P.	50.00000	Plan approved, <b>Contractor disagreed</b> to continue the work with agreed price, Informed by ZO
<b>COMPLETED</b>				
1	Bahraich	U.P.	99.35000	<b>Completed to be inaugurated</b>

## ANDHRA BANK - 7

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>1</b>	<b>0</b>	<b>1</b>	<b>3</b>	<b>1</b>	<b>1</b>

### ANDHRA

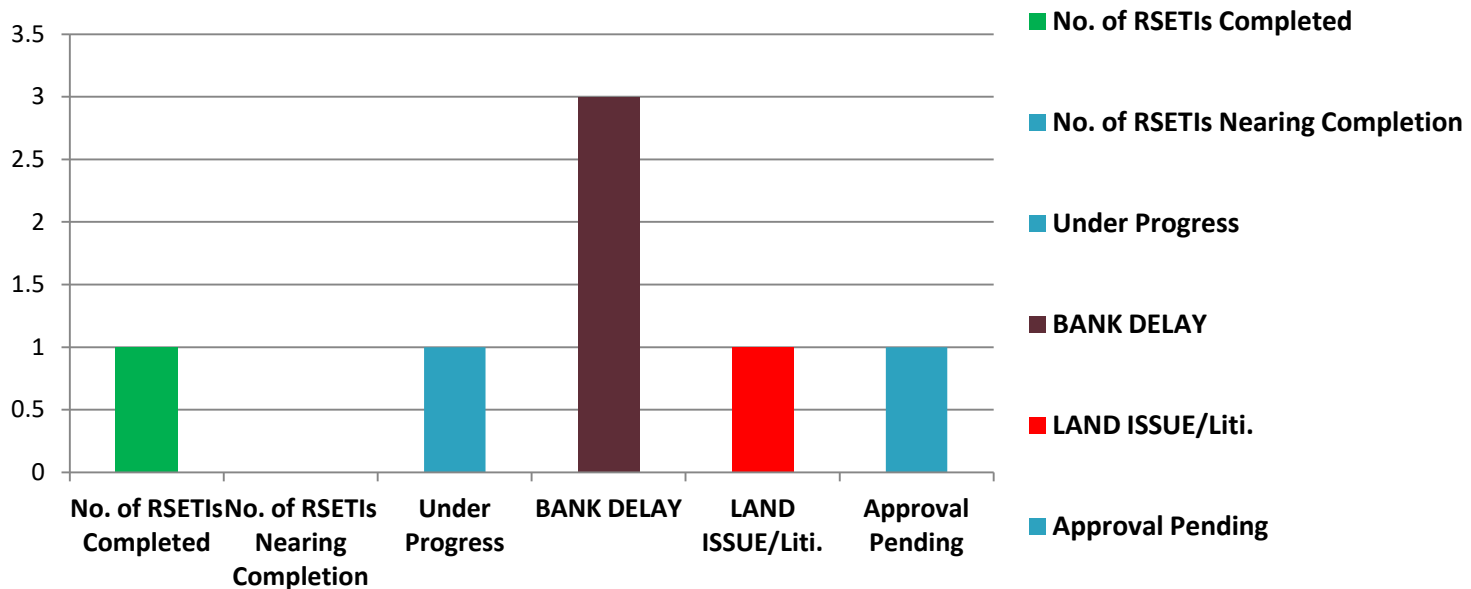


# ANDHRA BANK

S.NO	RSETI	STATE	FUNDS Released	STATUS	REMARKs
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>					
1	Krishna	Andhra Pradesh	50.00000	Alternate land yet to be allotted	Land allotted for the institute is not suitable for construction, <b>Alternate land yet to be allotted</b>
<b>BANK DELAY</b>					
1	Gajapati	Orissa	50.00000	BANK DELAY	<b>Contractor</b> yet to be appointed
2	Srikakulam	Andhra Pradesh	50.00000	BANK DELAY	<b>Contractor</b> yet to be appointed
3	Kasargod	Kerala	50.00000	OWN LAND - Bank Delay	<b>OWN LAND</b> <b>Contractor</b> yet to be appointed
<b>COMPLETED</b>					
1	West Godavari	Andhra Pradesh	88.78000	COMPLETED	<b>COMPLETED</b>
<b>APPROVAL PENDING</b>					
1	Ganjam	Orissa	50.00000	APPROVAL PENDING	<b>Approval plan is</b> in the process
<b>UNDER PROGRESS</b>					
1	East Godavari	Andhra Pradesh	50.00000	OWN LAND Under Process	OWN LAND, Contractor appointed, Construction of the <b>building started</b>



## APRB - 1

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>0</b>	<b>0</b>	<b>0</b>	<b>1</b>	<b>0</b>	<b>0</b>

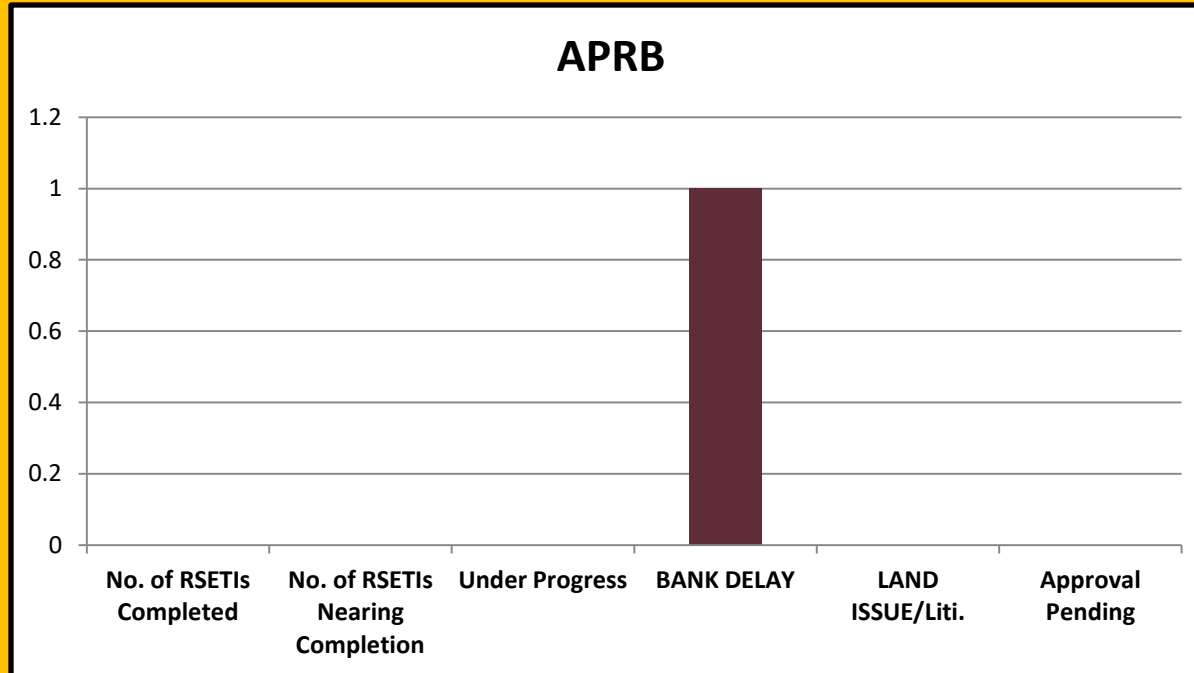


## ARUNACHAL PRADESH RURAL BANK

S.NO	RSETI	STATE	FUNDS Released	REMARKs
<b>BANK DELAY</b>				
1.	Papum Pare	Arunachal Pradesh	50.00000	DUE TO <b>OVER COST</b> ESTIMATION

## BANK OF BARODA - 40

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
18	4	5	4	6	3

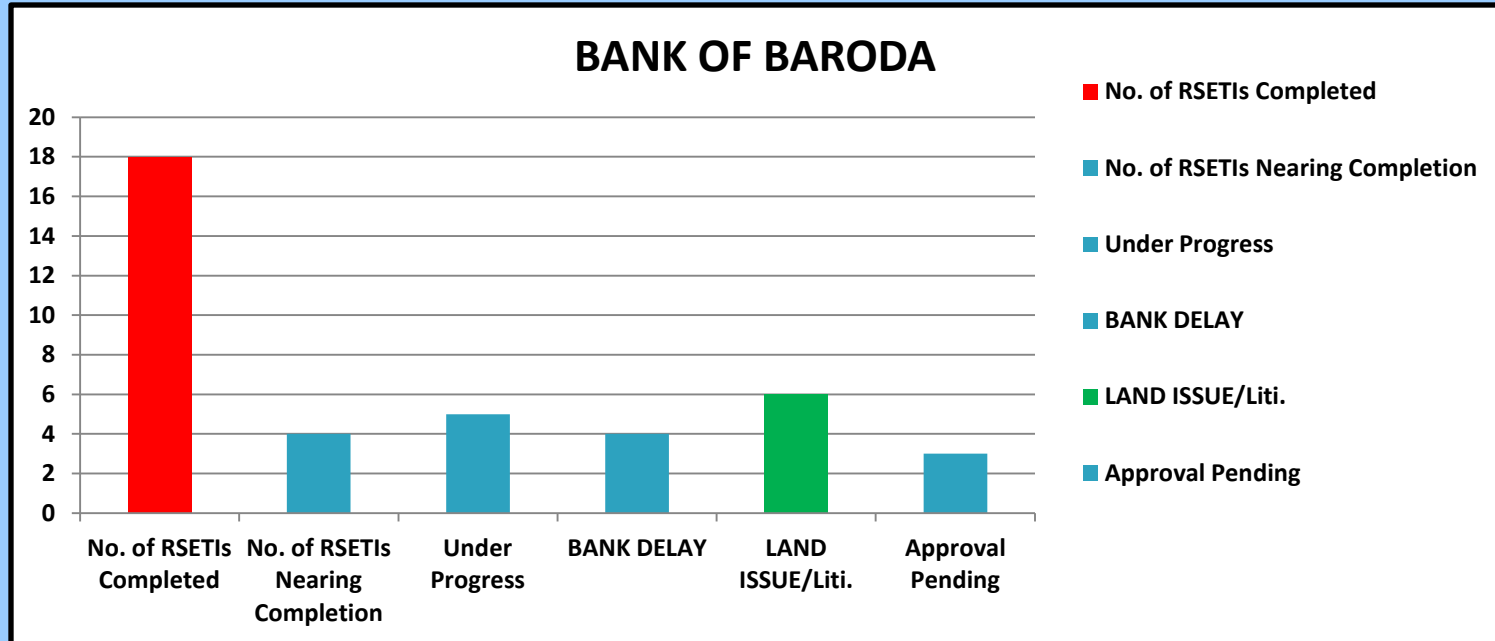

## BANK OF BARODA

S.NO	RSETI	STATE	FUNDS Released	STATUS
<b>APPROVAL PENDING</b>				
1	Panchmahal	Gujarat	50.00000	<b>Plan Estimate</b> being approved
2	Surat	Gujarat	50.00000	<b>Plan Estimate</b> being approved
3	Narmada	Gujarat	10.00000	<b>Plan Estimate</b> being approved
4	Pilibhit	U.P.	50.00000	<b>Map Approval Pending</b> with authority
<b>BANK DELAY</b>				
1	Sheohar	Bihar	50.00000	<b>BID Failed twice</b> , -TENDER to be FLOATED shortly
2	Sitmarhi	Bihar	50.00000	Architect to <b>prepare plan</b>
3	Sultanpur	U.P.	50.00000	<b>Tender Floted</b> for contractor
4	Pratapgarh	U.P.	50.00000	<b>Tender Floted</b> for contractor
<b>UNDER PROGRESS</b>				
1	Dangs	Gujarat	50.00000	Construction work started in <b>Oct 2017</b>
2	Baroda (Vadodara)	Gujarat	50.00000	NoC from airport authority granted <b>construction restarted</b>
3	Ambedkar Nagar	U.P.	50.00000	Under Process 1 <sup>st</sup> SLAP , <b>Revised estimate</b> for increased area is in progress construction
4	Allahabad	U.P.	50.00000	Construction started in <b>august 2017</b>
5	Shahjahanpur	U.P.	50.00000	Started in <b>september 2017</b>

# BANK OF BARODA

**Cont.**


S.NO	RSETI	STATE	FUNDS Released	STATUS
<b>LAND ISSUES/LITIGATIONs</b>				
1	Chittorgarh	Rajasthan	50.00000	<b>LAND CONVERSION IS PENDING/Ministry</b> approved the deviation of road passing through land
2	Churu	Rajasthan	50.00000	<b>MATTER IN HIGH COURT OF RAJASTHAN</b>
3	Sawai Madhopur	Rajasthan	50.00000	Previously <b>allotted land was disputed</b> , another land being identified
4	Faizabad	U.P.	50.00000	<b>Map approval pending</b> (DUE TO AGRI LAND ISSUE), Another land being identified
5	Bareilly	U.P.	50.00000	<b>Construction Stop</b> Due to green belt issue
6	Nainital	Uttarakhand	50.00000	Previous land was <b>disputed</b> , new land being identified
<b>NEARING COMPLETION</b>				
1	Dahod	Gujarat	50.00000	2 <sup>nd</sup> floor is completed <b>PLASTER WORK IS GOING ON</b>
2	Anand	Gujarat	100.00000	<b>Tiles for flooring</b> for 1st n 2nd floor completed
3	Fatehpur	U.P.	98.90737	<b>FINISHING STAGE</b>
4	Kanpur Dehat	U.P.	98.60990	<b>FINISHING STAGE</b>

**BANK OF BARODA****Cont.****COMPLETED RSETIs IN BoB**

1.	Gandhi Nagar	Gujarat	98.32318
2.	Bharuch	Gujarat	100.00000
3.	Navsari	Gujarat	100.00000
4.	Valsad/Bulsar)	Gujarat	50.00000
5.	Jhabua	Madhya Pradesh	100.00000
6.	Alirajpur	Madhya Pradesh	100.00000
7.	Ajmer	Rajasthan	100.00000
8.	Banswara	Rajasthan	100.00000
9.	Bundi	Rajasthan	100.00000
10.	Dungarpur	Rajasthan	100.00000
11.	Jhunjhunu	Rajasthan	50.00000
12.	Karauli	Rajasthan	50.00000
13.	Pratapgarh	Rajasthan	100.00000
14.	Tonk	Rajasthan	50.00000
15.	Raebareli	U.P.	99.33999
16.	Kanpur Nagar	U.P.	99.14994
17.	Gauriganj (Amethi)	U.P.	99.84093
18.	Udhamsingh Nagar	Uttarakhand	100.00000

## BANK OF INDIA - 40

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
13	21	1	2	3	0

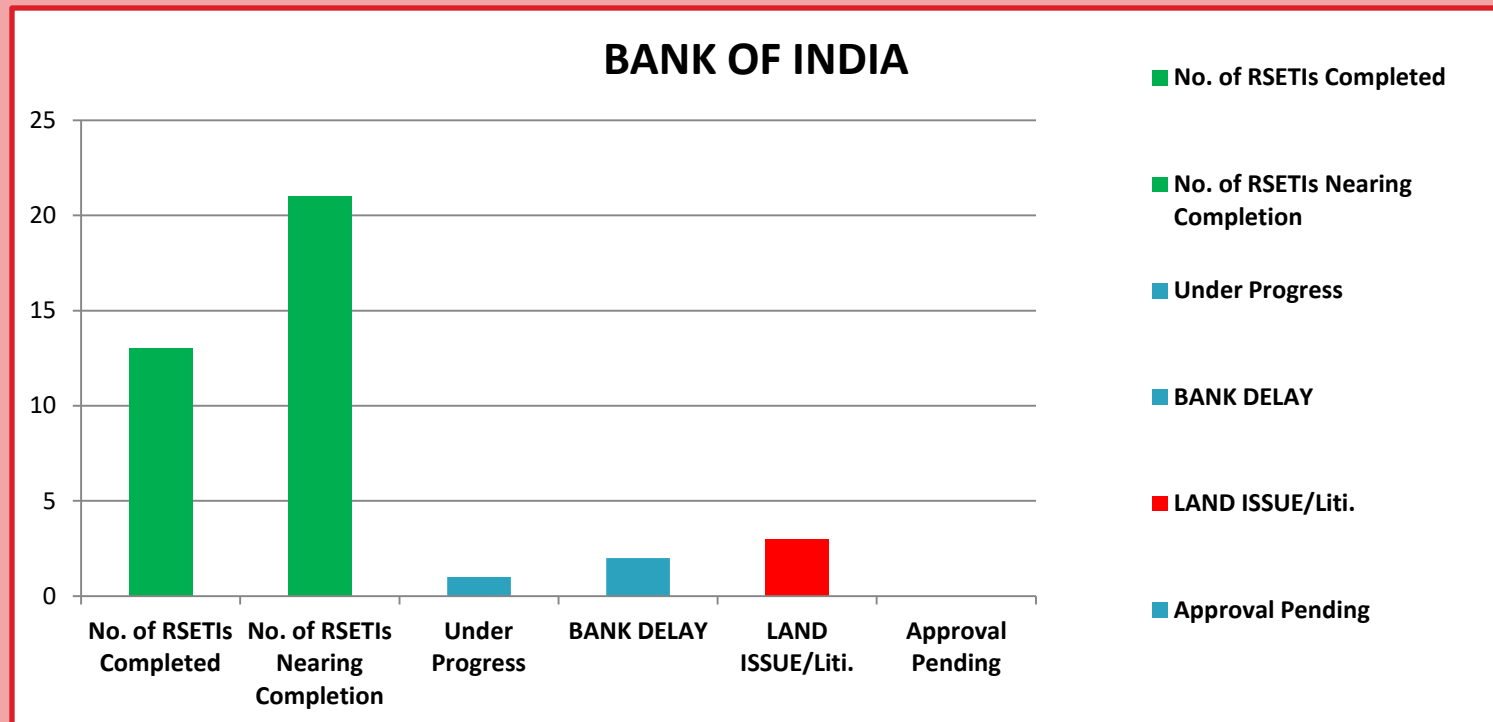

## BANK OF INDIA

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Kolhapur	Maharashtra	50.00000	MoU signed & Possession Taken
2	Unnao	U.P.	50.00000	Contractor have been appointed
<b>LAND ISSUE/LITIGATIONs</b>				
1	Raigad	Maharashtra	50.00000	Collector office informed that maximum permissible construction is <b>435.80 Sq. meter</b> only
2	Wardha	Maharashtra	50.00000	LAND DISPUTE CASE/ <b>Court Case</b>
3	Farrukhabad	U.P.	50.00000	LAND DISPUTE CASE/ <b>Court Case</b>
<b>UNDER PROGRESS</b>				
1	Hardoi	U.P.	50.00000	Likely to be complete on <b>30.6.2018</b>

**BANK OF INDIA****Cont.****COMPLETED**

1	Bokaro	Jharkhand	100.00000	SHIFTED IN NEW PREMISES
2	Koderma	Jharkhand	100.00000	SHIFTED IN NEW PREMISES
3	Burhanpur	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
4	Dewas	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
5	Dhar	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
6	East Nimar (Khandwa)	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
7	West Nimar (Khargone)	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
8	Rajgarh	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
9	Ujjain	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
10	Barwani	Madhya Pradesh	100.00000	SHIFTED IN NEW PREMISES
11	Solapur	Maharashtra	100.00000	SHIFTED IN NEW PREMISES
12	Keonjhar	Orissa	100.00000	SHIFTED IN NEW PREMISES
13	Mayurbhanj/ Baripada	Orissa	100.00000	SHIFTED IN NEW PREMISES
14	Khunti	Jharkhand	100.00000	COMPLETED




**BANK OF INDIA INDIA****Cont.****NEARING COMPLETION**

1	Chatra	Jharkhand	100.00000	31.12.2017
2	Dhanbad	Jharkhand	79.98175	31.1.2018
3	East Singhbhum	Jharkhand	100.00000	31.1.2018
4	Giridh	Jharkhand	100.00000	31.1.2018
5	Gumla	Jharkhand	100.00000	31.1.2018
6	Lohardaga	Jharkhand	100.00000	31.1.2018
7	Simdega	Jharkhand	100.00000	31.1.2018
8	West Singhbhum	Jharkhand	90.59397	31.1.2018
9	Sehore	Madhya Pradesh	50.00000	31.3.2018
10	Shajapur	Madhya Pradesh	100.00000	31.1.2018
11	Bhandara	Maharashtra	88.79091	31.1.2018
12	Chandrapur	Maharashtra	50.00000	31.1.2018 (2nd Installment not received)
13	Gadchiroli	Maharashtra	78.09000	31.1.2018
14	Ratnagiri	Maharashtra	100.00000	31.1.2018
15	Sangli	Maharashtra	50.00000	31.3.2018
16	Sindhudurg	Maharashtra	84.65156	28.2.2018
17	Barabanki	U.P.	50.00000	30.3.2018/2nd Installment not received
18	Kannauj	U.P.	96.50476	31.3.2018
19	Lucknow	U.P.	50.00000	31.3.2018 - Visiting by RNL on next week - going to release
20	Mainpuri	U.P.	99.83562	31.3.2018

## BANK OF MAHARASHTRA - 6

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>0</b>	<b>0</b>	<b>1</b>	<b>0</b>	<b>1</b>	<b>4</b>

### BOM

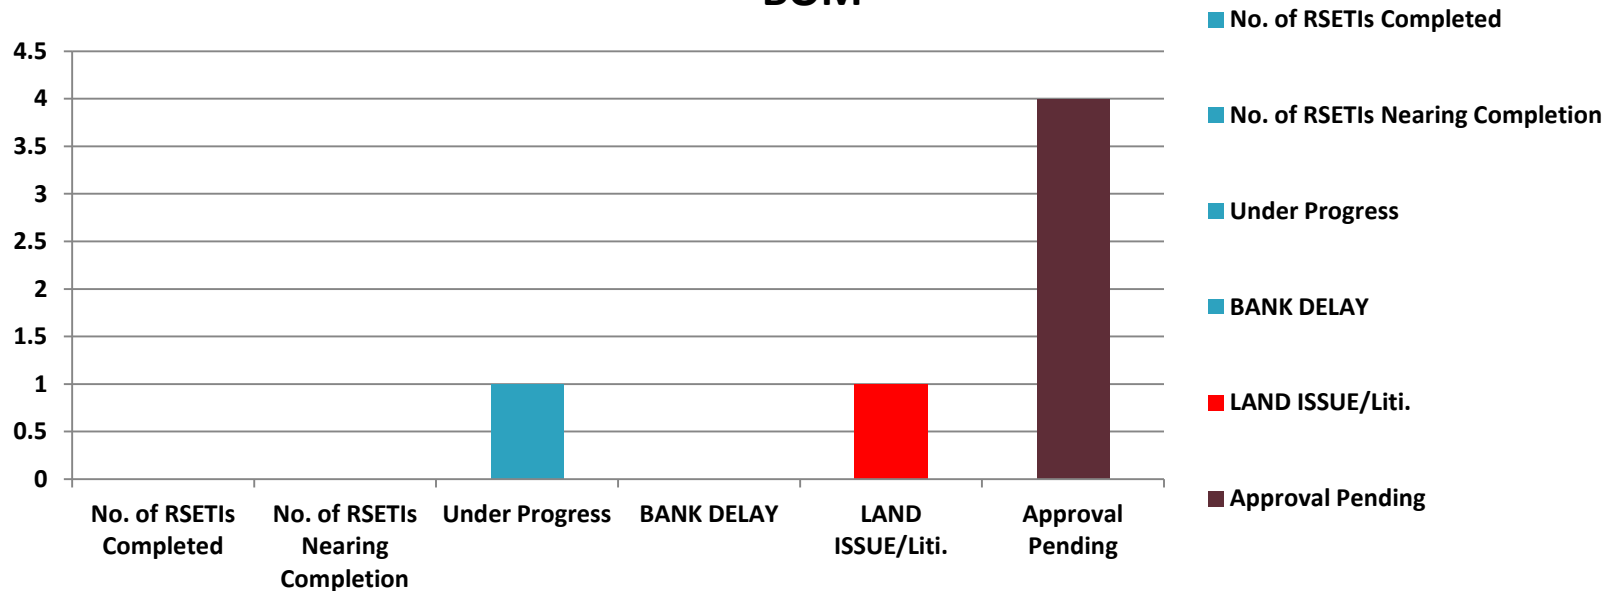

# BANK OF MAHARASHTRA

## ALTERNATE LAND YET TO BE ALLOTTED

1	Amravathi	Maharashtra	50.00000	Earlier land is not suitable, <b>alternate land yet to be allotted.</b>
---	-----------	-------------	----------	---

## APPROVAL PENDING

1	Aurangabad	Maharashtra	50.00000	Sanction of plan is awaited from <b>CIDCO</b> , since 28.2.2017.
2	Jalna	Maharashtra	50.00000	Bldg construction permission is expected from nagar parishad during current quarter, formalities will be completed with in 2 weeks
3	Nagpur	Maharashtra	50.00000	Development Authority has raised queries in <b>sanction of layout plan</b> details is given 1.7.2017
4	Pune	Maharashtra	50.00000	We have just got WAIVER OF FIRE NoC letter from PMRDA


## UNDER PROGRESS

1	Nasik	Maharashtra	100.00000	Work is in <b>progress</b>
---	-------	-------------	-----------	----------------------------

## CANARA - 18

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>10</b>	<b>0</b>	<b>1</b>	<b>4</b>	<b>2</b>	<b>1</b>

### CANARA

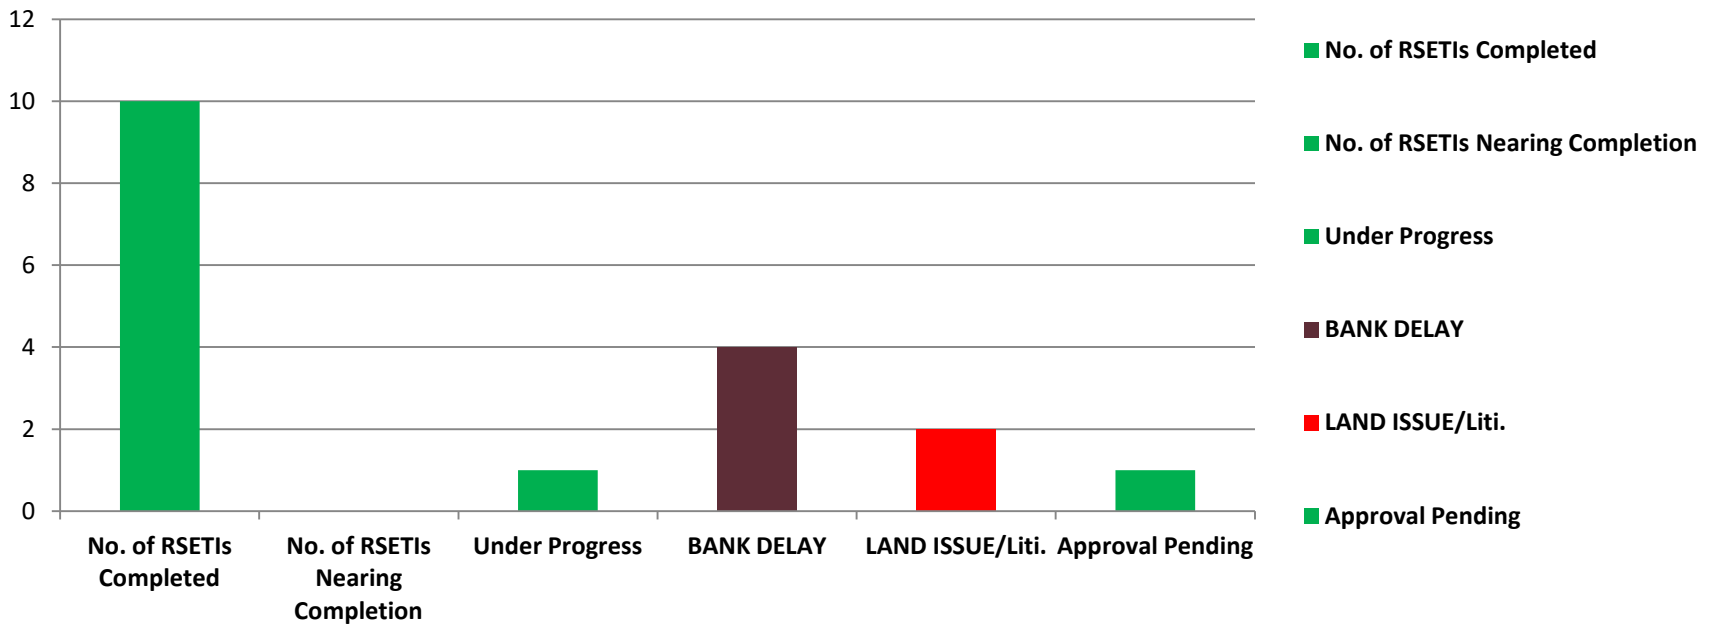

## CANARA

S.NO	RSETI	STATE	FUNDS Released	REMARKS
<b>UNDER PROGRESS</b>				
1	Sheikpura	Bihar	50.00000	Civil works of ground floor portion up to roof level is constructed and <b>roof slab to be casted</b>
<b>APPROVAL PENDING</b>				
1	Coimbatore	Tamilnadu	17.50000	<b>Plan approval pending</b> from Local Town Planning Authority
<b>BANK DELAY</b>				
1	Dindigul	Tamilnadu	50.00000	<b>Floor Plans</b> Preparation is underway
2	Theni	Tamilnadu	50.00000	<b>Floor Plans</b> Preparation & Estimation of works are underway
3	Etah	U.P.	50.00000	<b>Floor Plans</b> Preparation & Estimation of works are underway
4	Kanshiramnagar	U.P.	50.00000	<b>Floor Plans Preparation</b> & Estimation of works are underway
<b>ALTERNATE LAND YET TO BE ALLOTTED/LAND YET TO BE ALLOTTED</b>				
1	Thirupur	Tamilnadu	50.00000	Allotted land is not suitable, <b>ALTERNATE Land</b> yet to be allotted.
2	Erode	Tamilnadu	10.00000	<b>ALTERNATE</b> Land Yet to be allotted
3	Niligirs	Tamilnadu	10.00000	<b>Land Yet to be allotted</b>


## CANARA

Cont.

S.NO	RSETI	STATE	FUNDS Released	REMARKS
<b>COMPLETED</b>				
1	Chikballapur	Karnataka	100.00000	COMPLETED
2	Davengare	Karnataka	100.00000	COMPLETED
3	Hassan	Karnataka	100.00000	COMPLETED
4	Kolar	Karnataka	100.00000	COMPLETED
5	Shimoga	Karnataka	100.00000	COMPLETED
6	Mallapuram	Kerala	100.00000	COMPLETED
7	Thirssur	Kerala	100.00000	COMPLETED
8	Sivagangai	Tamilnadu	100.00000	COMPLETED
9	Aligarh	U.P.	100.00000	COMPLETED
10	Hathras	U.P.	85.68442	Likely to be sifted by end of july2017
<b>LITIGATIONs</b>				
1	Ramanagara	Karnataka	40.00000	Construction Stop by Forest Dept. <b>The issue in the court</b>

## CENTRAL BANK OF INDIA - 44

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
30	3	3	1	1	6

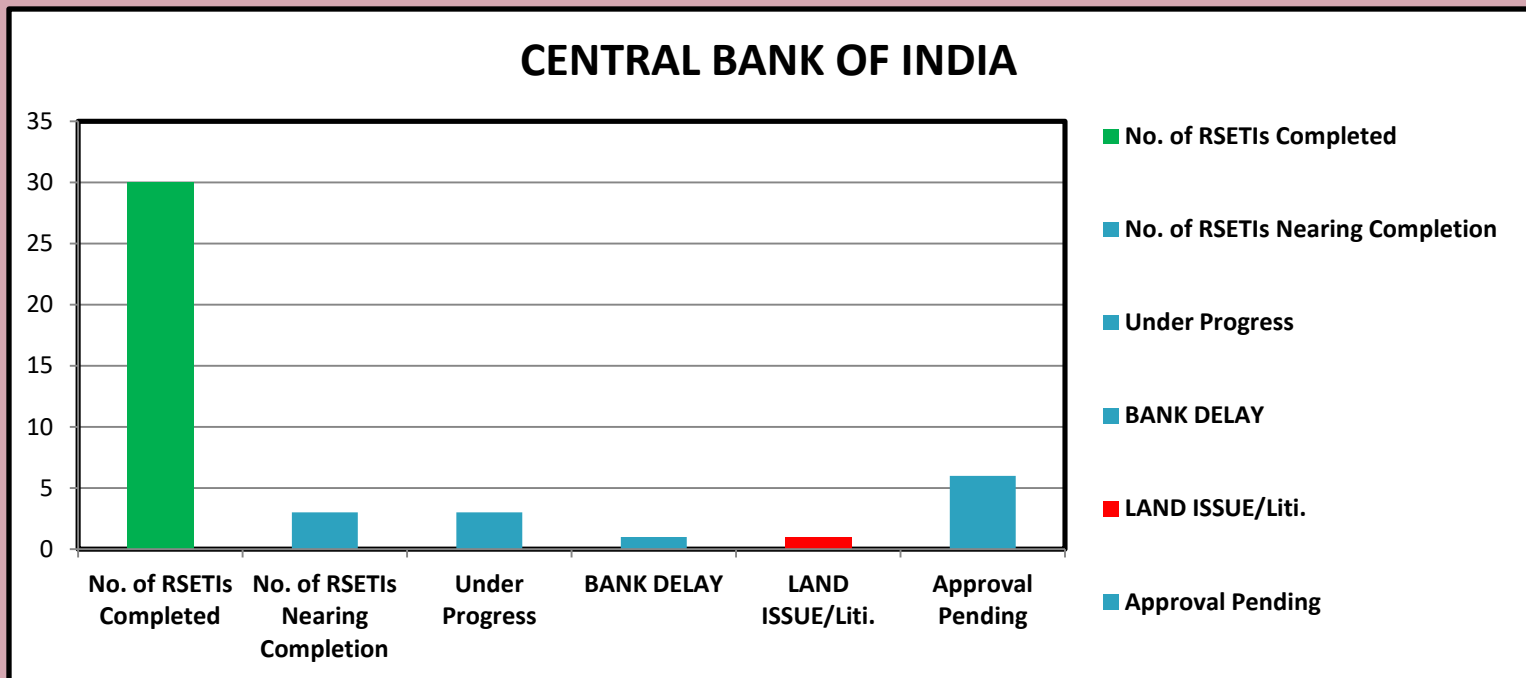

# CENTRAL BANK OF INDIA

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Tinsukia	Assam	50.00000	Construction up to ground floor is completed and work is going on
2	Auraiya	U.P.	50.00000	Ground floor completed & 2nd floor slab completed
3	Ballia	U.P.	50.00000	High voltage wire running over the bldg, process for removal of wire is going on
<b>UNDER PROGRESS</b>				
1	Muzaffarpur	Bihar	50.00000	Work is in progress
2	Etawah	U.P.	50.00000	Ground floor slab completed
3	Kushi Nagar	U.P.	50.00000	Ground floor pillar work is in process
<b>APPROVAL PENDING</b>				
1	Bhind	Madhya Pradesh	50.00000	Statutory approval is in process
2	Akola	Maharashtra	50.00000	Statutory approval is in process
3	Buldhana	Maharashtra	50.00000	Statutory approval is in process
4	Deogarh	Orissa	50.00000	Statutory approval is in process
5	Cooch Behar	West Bengal	50.00000	Statutory approval is in process
6	Darjeeling	West Bengal	50.00000	Statutory approval is in process
<b>BANK DELAY</b>				
1	Dhule	Maharashtra	50.00000	Tendering process completed & work order has been issued
<b>LAND YET TO BE ALLOTTED/POSSESSION YET TO BE TAKEN</b>				
1	Jalpaiguri	West Bengal	10.00000	Land has been identified by DA, GoWB has to finalize the proposal of land
2	Ahmedabad	Maharashtra	50.00000	Possession yet to be taken




**CENTRAL BANK OF INDIA**

Cont.

<b>S.No</b>	<b>RSETIS</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>
<b>COMPLETED</b>			
1	Darbhanga	Bihar	93.07900
2	East Champaran	Bihar	93.84993
3	Gopalganj	Bihar	93.42370
4	Katihar	Bihar	50.00000
5	Madhubani	Bihar	89.06873
6	Saran	Bihar	91.41770
7	Siwan,	Bihar	97.70930
8	West Champaran	Bihar	91.80520
9	Koria	Chhattisgarh	100.00000
10	Surguja	Chhattisgarh	100.00000
11	Anuppur	Madhya Pradesh	84.05890
12	Balaghat	Madhya Pradesh	100.00000
13	Betul	Madhya Pradesh	100.00000
14	Chhindwara	Madhya Pradesh	100.00000
15	Dindori	Madhya Pradesh	100.00000
16	Gwalior	Madhya Pradesh	100.00000
17	Hoshangabad	Madhya Pradesh	100.00000
18	Jabalpur	Madhya Pradesh	100.00000
19	Mandla	Madhya Pradesh	100.00000
20	Mandsaur	Madhya Pradesh	50.00000
21	Morena	Madhya Pradesh	100.00000
22	Narsinghpur	Madhya Pradesh	100.00000
23	Raisen	Madhya Pradesh	100.00000
24	Ratlam	Madhya Pradesh	100.00000
25	Sagar	Madhya Pradesh	100.00000
26	Seoni	Madhya Pradesh	100.00000
27	Shahdol	Madhya Pradesh	100.00000
28	Jalgaon	Maharashtra	100.00000
29	Yavatmal	Maharashtra	87.40000
30	Kota	Rajasthan	100.00000

## CORPORATION BANK - 2


No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
2	0	0	0	0	0

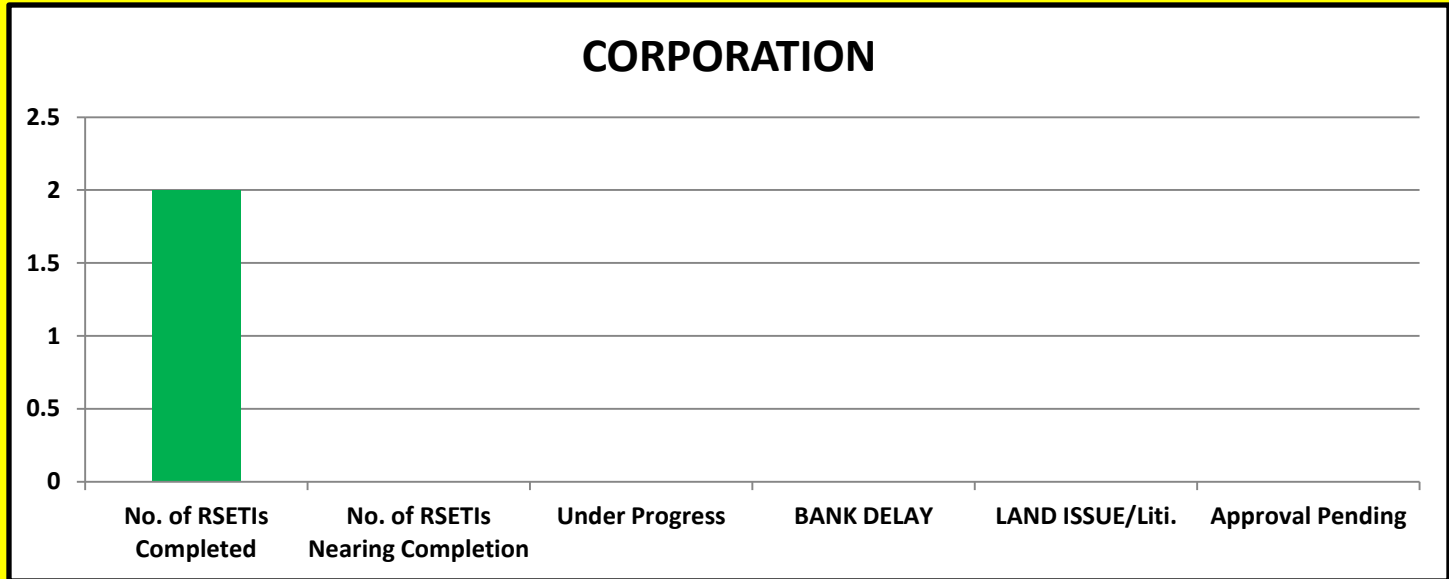

## CORPORATION BANK

S.NO	RSETI	STATE	FUNDS RELEASED
<b>COMPLETED</b>			
1	Chikmagalur	Karnataka	60.00000
2	Kodagu	Karnataka	100.00000


<b>DCC BANK - 1</b>					
<b>No. of RSETIs Completed</b>	<b>No. of RSETIs Nearing Completion</b>	<b>Under Progress</b>	<b>BANK DELAY</b>	<b>LAND ISSUE/Liti.</b>	<b>Approval Pending</b>
<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>

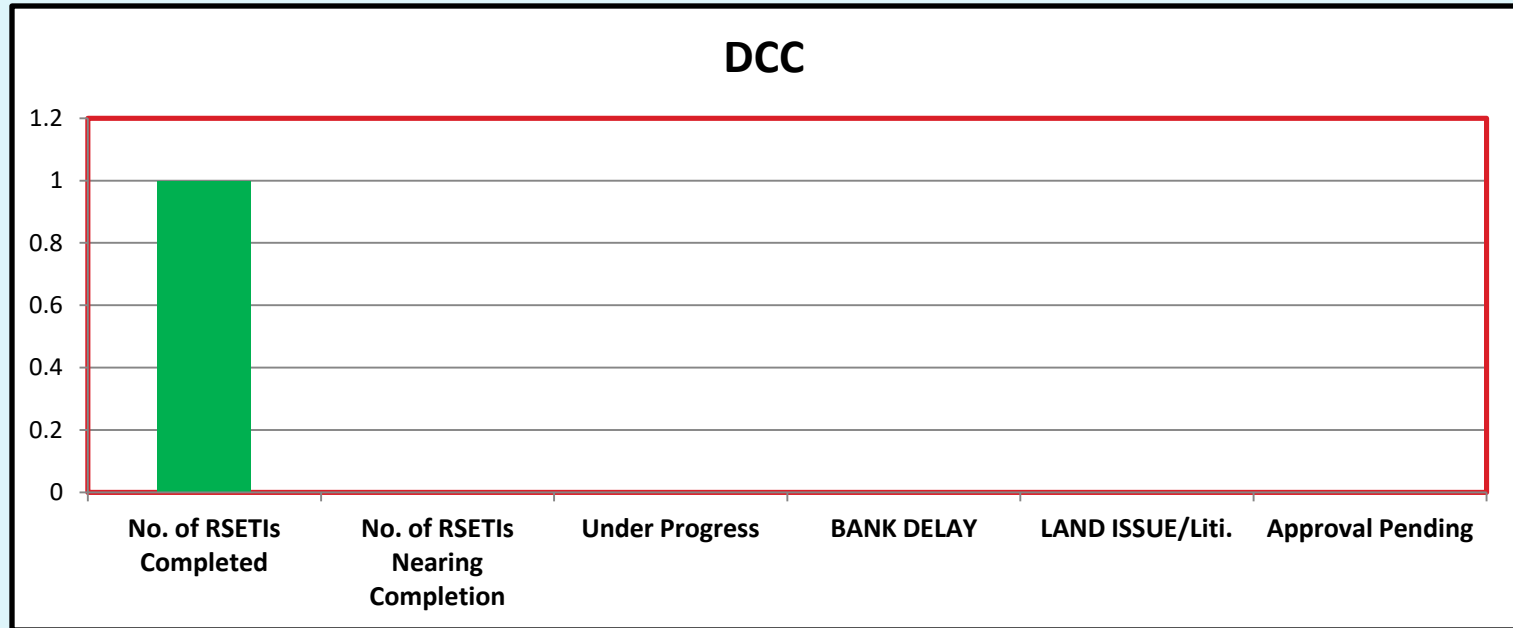

<b>DCC BANK</b>			
<b>S.NO</b>	<b>RSETI</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>
<b>COMPLETED</b>			
<b>1</b>	Bidar	Karnataka	99.03000

## ICICI BANK - 2

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
1	0	1	0	0	0

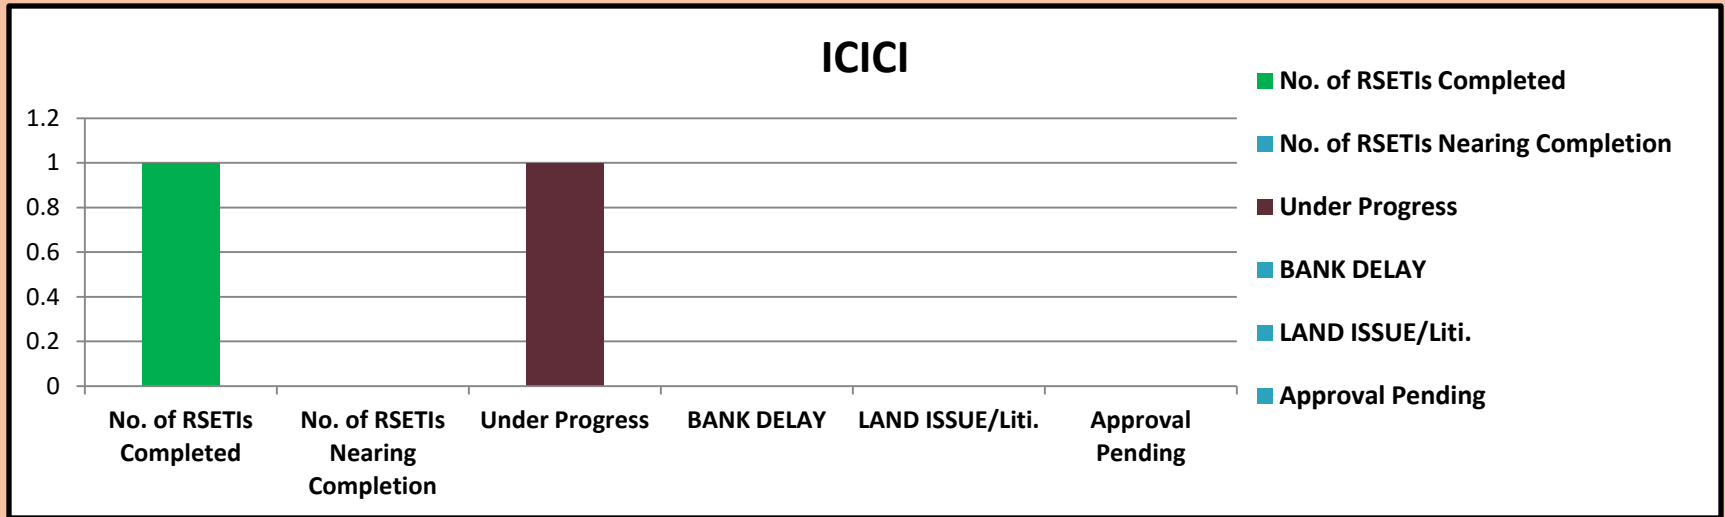


## ICICI BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	Jodhpur	Rajasthan	50.00000	Construction started on 22nd June, 2017, <b>water and electricity facilities not available</b> , pursuing with jodhpur development authority at various level
<b>COMPLETED</b>				
1	Udaipur	Rajasthan	100.00000	COMPLETED

## DENA BANK - 12


No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
8	2	0	1	0	1

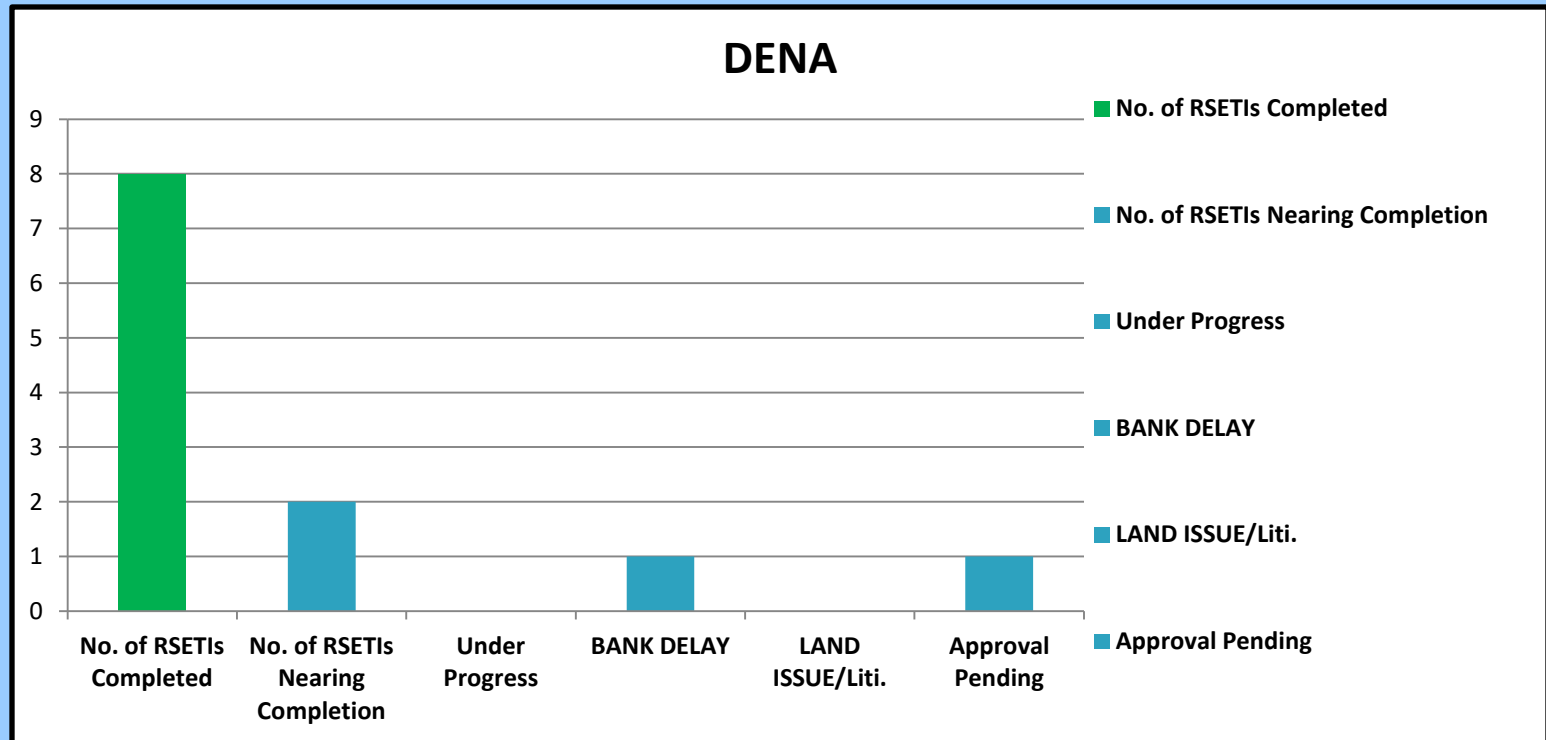

## DENA BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Durg	Chhattisgarh	100.00000	<b>NEARING COMPLETED - 31.1.2018</b> <b>contractor has been stopped the construction</b>
2	Mahasamund	Chhattisgarh	90.48000	<b>NEARING COMPLETED - 30.1.2017</b>
3	Raipur	Chhattisgarh	50.00000	<b>Land Allotted on 15.12.2017</b>
<b>APPROVAL PENDING</b>				
1	Ahmedabad	Gujarat	50.00000	<b>Construction Plan not yet approved by NRDA</b>
<b>COMPLETED</b>				
1	Dhamtari,	Chhattisgarh	100.00000	COMPLETED - 31.12.2015
2	Rajnandgaon	Chhattisgarh	100.00000	SHIFTED ON 31 MAY 2016
3	Banaskantha	Gujarat	100.00000	SHIFTED ON 31 MAY 2016
4	Kutch (Bhuj)	Gujarat	100.00000	SHIFTED ON 8 AUGUST 2016
5	Mehsana	Gujarat	100.00000	SHIFTED ON 6TH SEPT. 2016
6	Patan	Gujarat	100.00000	SHIFTED ON 25TH AUGUST, 2014
7	Sabarkantha	Gujarat	100.00000	SHIFTED ON 1 OCT 2016
8	Silvassa, D&n Haveli,	U.T.	87.19000	SHIFTED ON 3.7.2017


IDBI BANK - 1					
No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
0	0	0	0	0	1

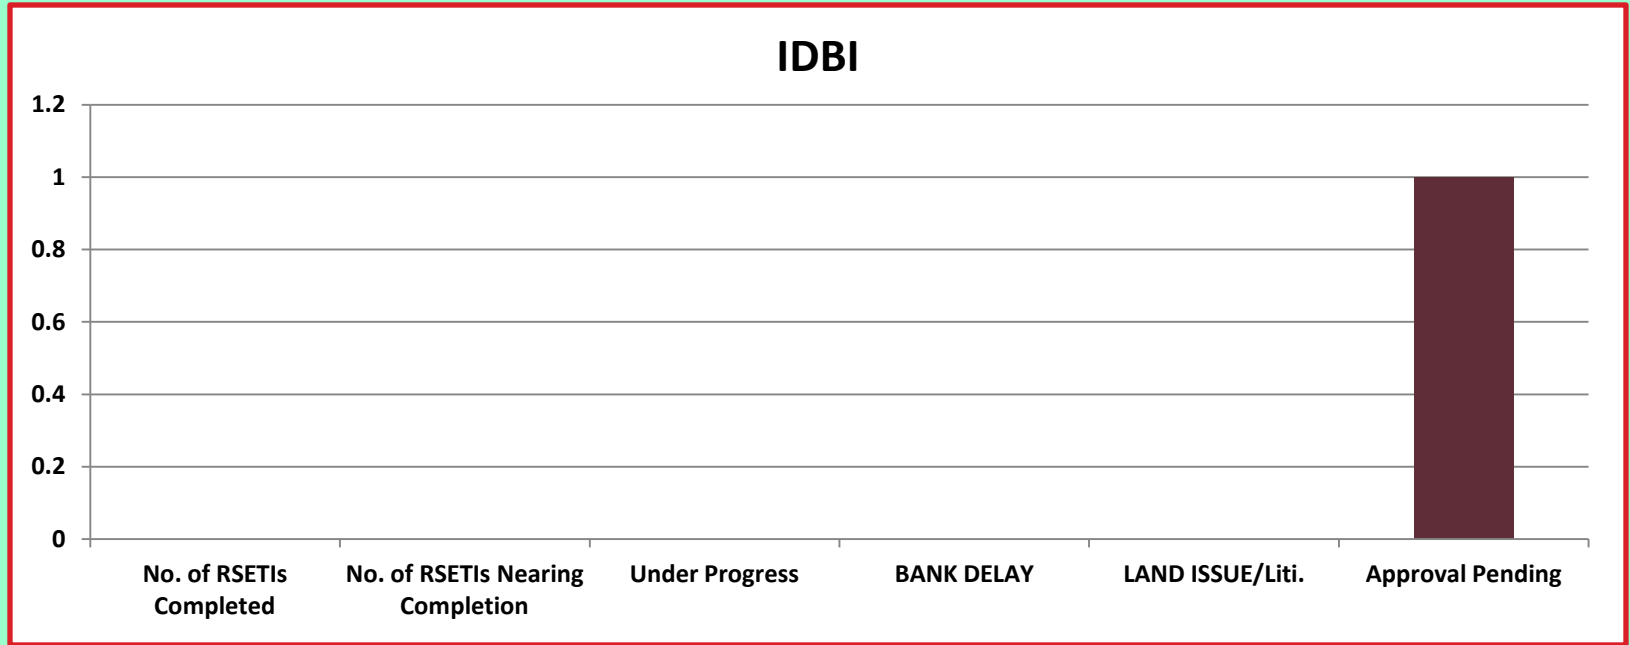

IDBI BANK				
S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>APPROVAL PENDING</b>				
1	Satara	Maharashtra	50.00000	Building plan & Estimate are under <b>approval process</b>

## KOTAK MAHINDRA BANK - 1

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>

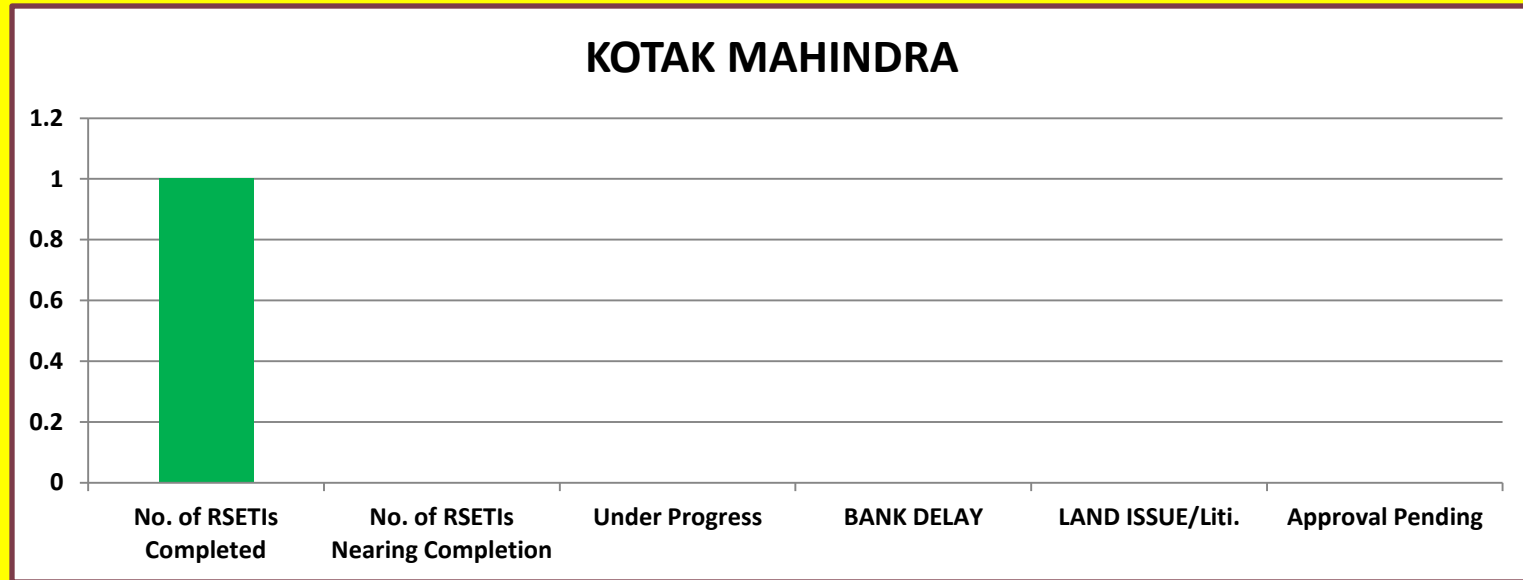

## KOTAK MAHINDRA BANK


S.No	RSETI	STATE	FUNDS RELEASED
<b>COMPLETED</b>			
1	Bagalkot	Karnataka	100.00000



## INDIAN OVERSEAS BANK - 6

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
0	0	0	1	0	5


### IOB

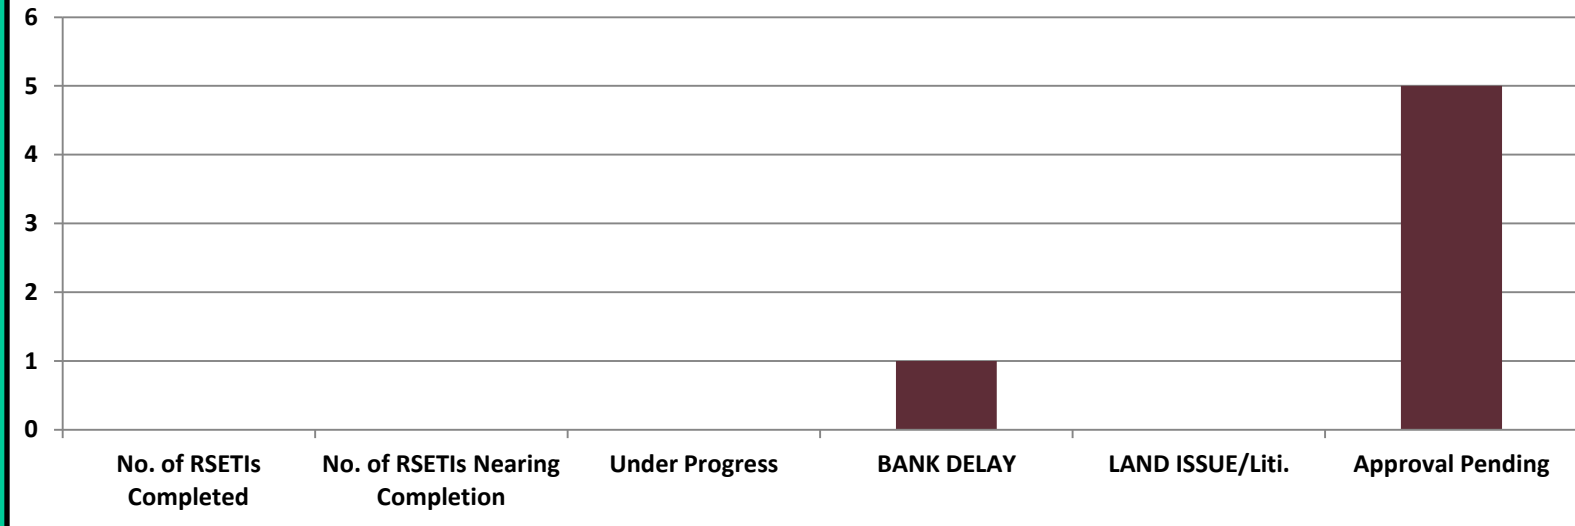

## INDIAN OVERSEAS BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Tiruvananthapuram	Kerala	50.00000	Float the tender for construction of the bldg & corporation of Trivandrum has informed that the approached road width is 2.40mts (against the required 3.60mts) which is not sufficient to obtain bldg permit for construction.
<b>APPROVAL PENDING</b>				
1	Perambalur	Tamilnadu	50.00000	Sumbitted plan to <b>LPA/TPA for approval</b>
2	Tanjavur	Tamilnadu	50.00000	Sumbitted plan to <b>LPA/TPA for approval</b>
3	Kanyakumari	Tamilnadu	50.00000	Sumbitted plan to <b>LPA/TPA for approval</b>
4	Pudukottai	Tamilnadu	50.00000	Sumbitted plan to <b>LPA/TPA for approval</b>
5	Thiruchirapalli	Tamilnadu	50.00000	Sumbitted plan to <b>LPA/TPA for approval</b>

INDIAN BANK - 5					
No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
0	0	0	0	3	2

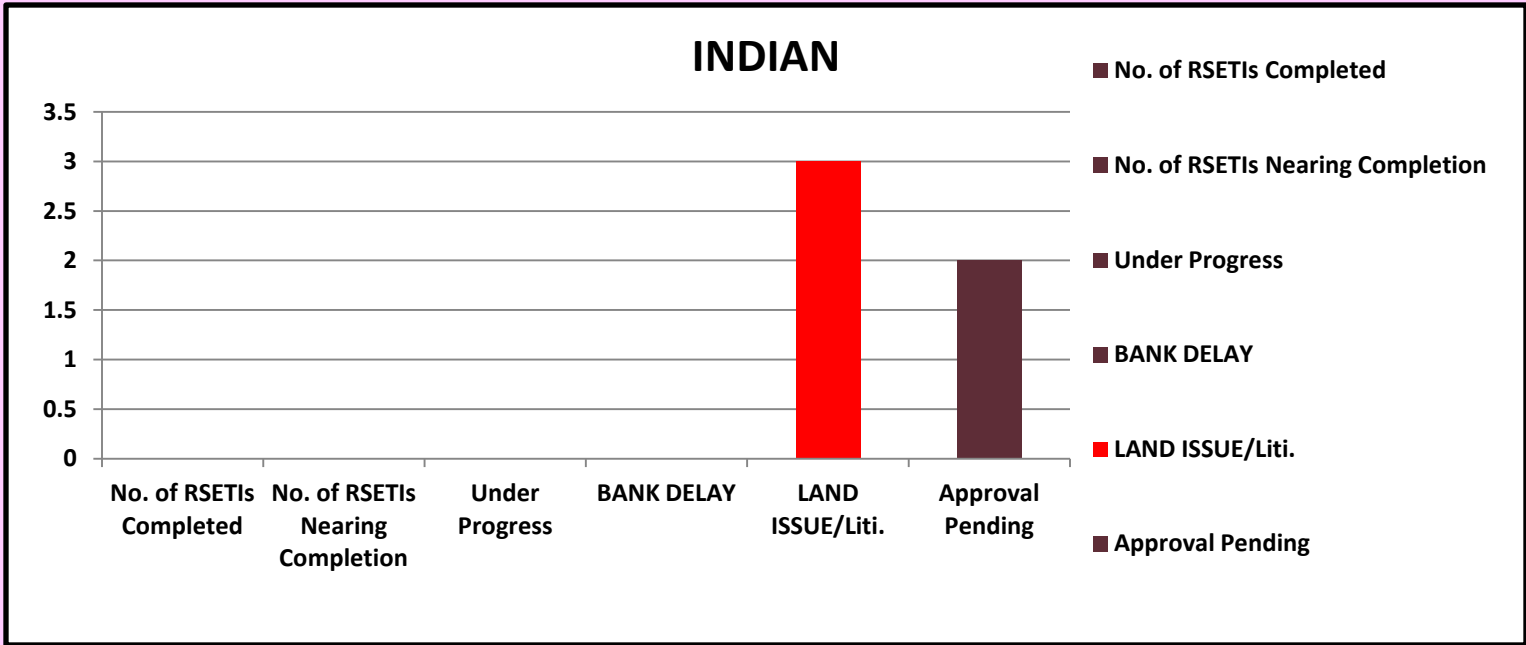


# INDIAN BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>APPROVAL PENDING</b>				
1	Kanchipuram	Tamilnadu	50.00000	Architect Appointed, <b>Plan Approval Under Process</b>
2	Thiruvannamalai	Tamilnadu	50.00000	<b>Plan approval pending</b>
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Vellore	Tamilnadu	50.00000	Original land allotted and taken back by govt. & alternate land identified opposite to Vellore institute of technology, <b>the signing of MoU is pending</b>
2	Namakkal	Tamilnadu	50.00000	The original land allotted to INDSETI is re-allotted to Agri. Department by the Govt. <b>Alternate site yet to be allotted</b>
<b>LAND ISSUES</b>				
1	Thiruvallure	Tamilnadu	50.00000	<b>ORIGINAL LAND ALLTD WAS TAKEN BACK BY GOVT.</b> ALTERNATE LAND identified for which official communication is yet to be received from the govt.
<b>LAND YET TO BE ALLOTTED</b>				
1	Salem	Tamilnadu	10.00000	<b>Land Yet to be allotted</b>
2	Puducherry	U.T.	10.00000	<b>Land Yet to be allotted</b>

## MEGHALAYA RURAL BANK (MRB) - 1

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
0	0	0	1	0	0

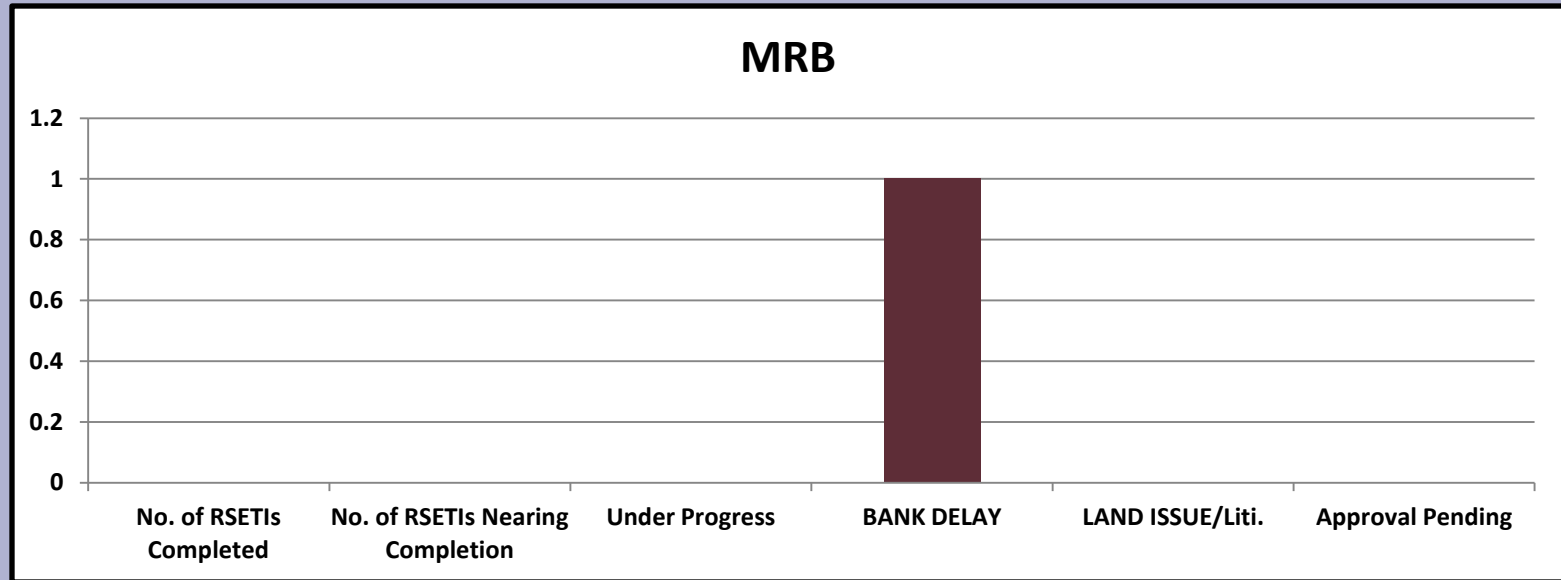


## MEGHALAYA RURAL BANK (MRB) - 1

S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	West Khasi Hills	Meghalaya	50.00000	<b>Architect Yet to be Appointed,</b> Funds yet to be Received

## ORIENTAL BANK OF COMMERCE - 4

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>2</b>	<b>0</b>	<b>1</b>	<b>0</b>	<b>1</b>	<b>0</b>

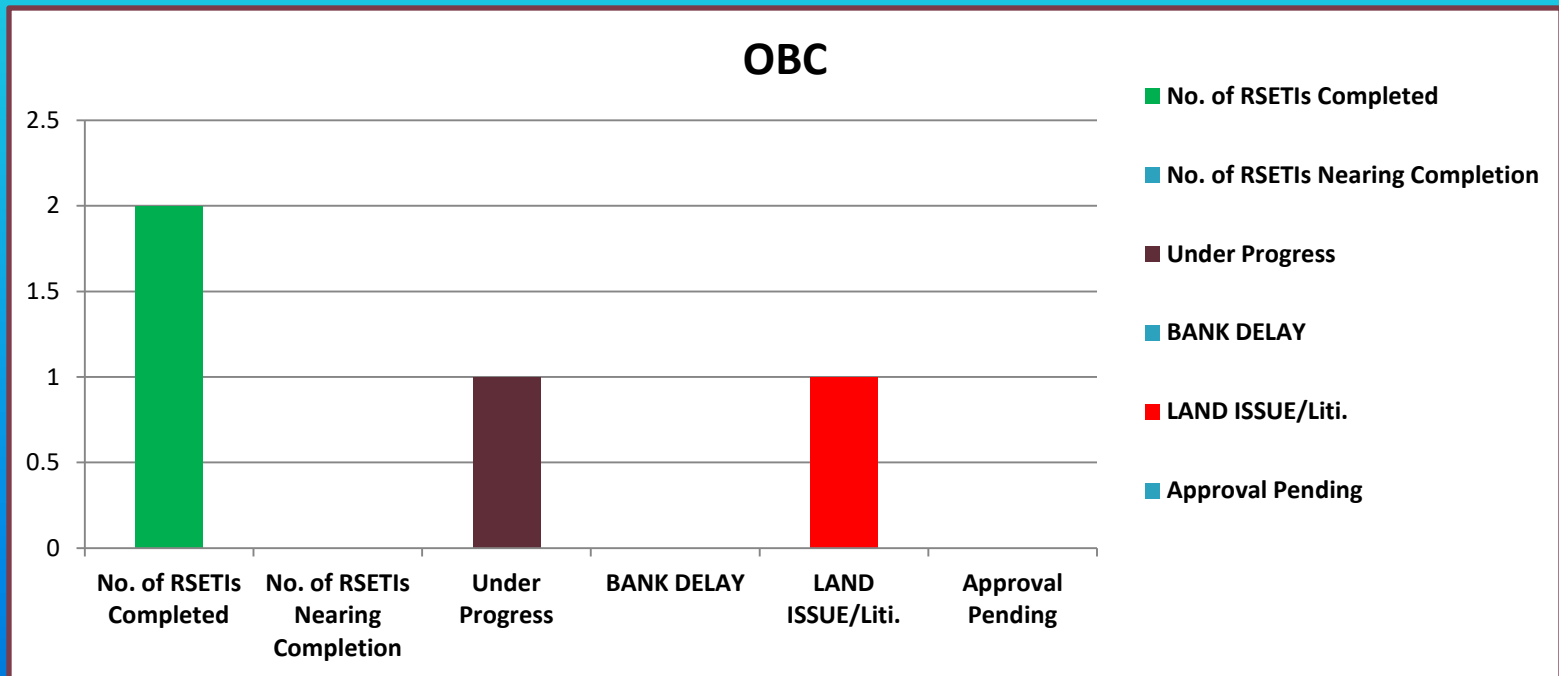


## OREINTAL BANK OF COMMERCE (OBC)

S.No	RSETI	STATE	FUNDs RELEASED	REMARKS
<b>COMPLETED</b>				
1	Ferozepur	Punjab	100.00000	<b>BLD COMPLETED</b> , TRAINING PROGRAMME ARE BEING CONDUCTED
2	Palwal	Haryana	100.00000	Inaugurated on 26.9.2017
<b>UNDER PROGRESS</b>				
1	Sri Ganga Nagar	Rajasthan	50.00000	Construction <b>Under Progress</b>
<b>LITIGATIONs</b>				
1	Dehradun	Uttarakhand	50.00000	CONSTRUCTION STARTED ON EARLIER ALLOTTED LAND, DUE TO NATURAL CALAMITY IN STATE, HIGH COURT JUDMENT, STOPPED THE WORK, <b>Allotted alternate land even there is a problem of accessibility</b>

## PUNJAB AND SIND BANK - 3

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
2	1	0	0	0	0

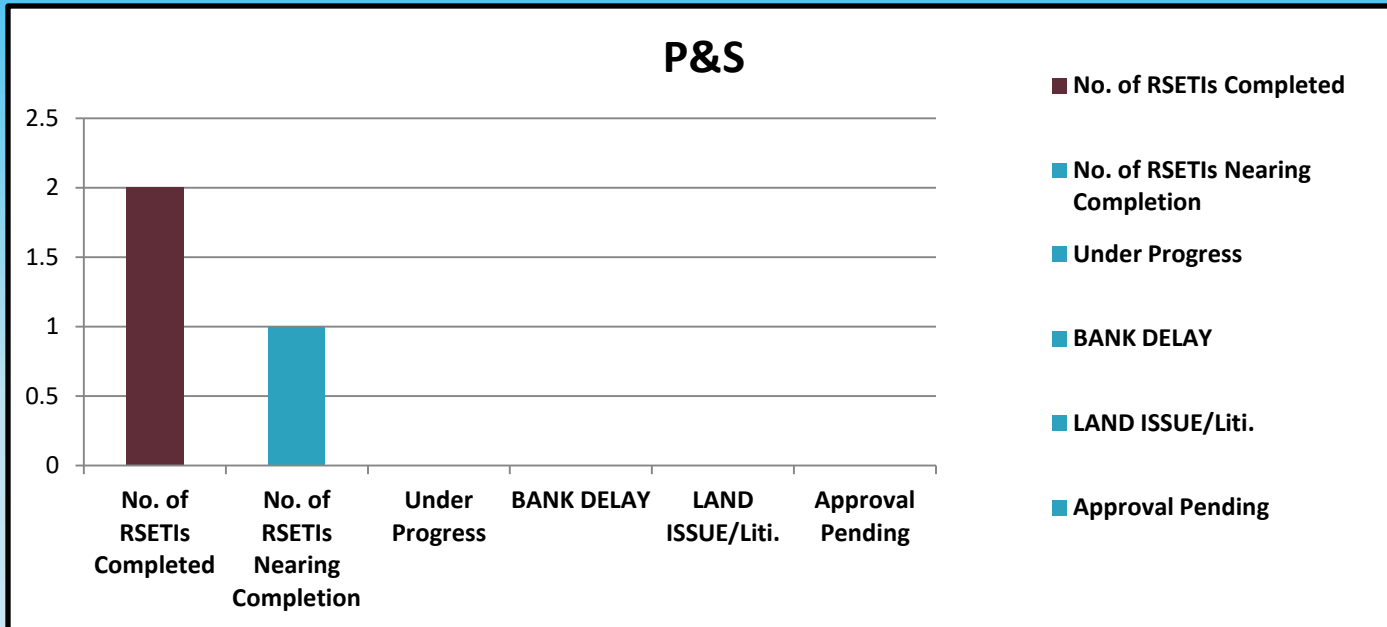


## P & S BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>COMPLETED</b>				
1	Faridkot	Punjab	100.00000	<b>COMPLETED - 31.5.2017</b>
2	Moga,	Punjab	100.00000	<b>COMPLETED -24.3.2014</b>
<b>NEARING COMPLETION</b>				
1	Ludhiana	Punjab	89.07000	<b>31-3-2018</b> LIKELY TO BE CMPLT



## VIJAYA BANK - 4

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
2	1	1	0	0	0

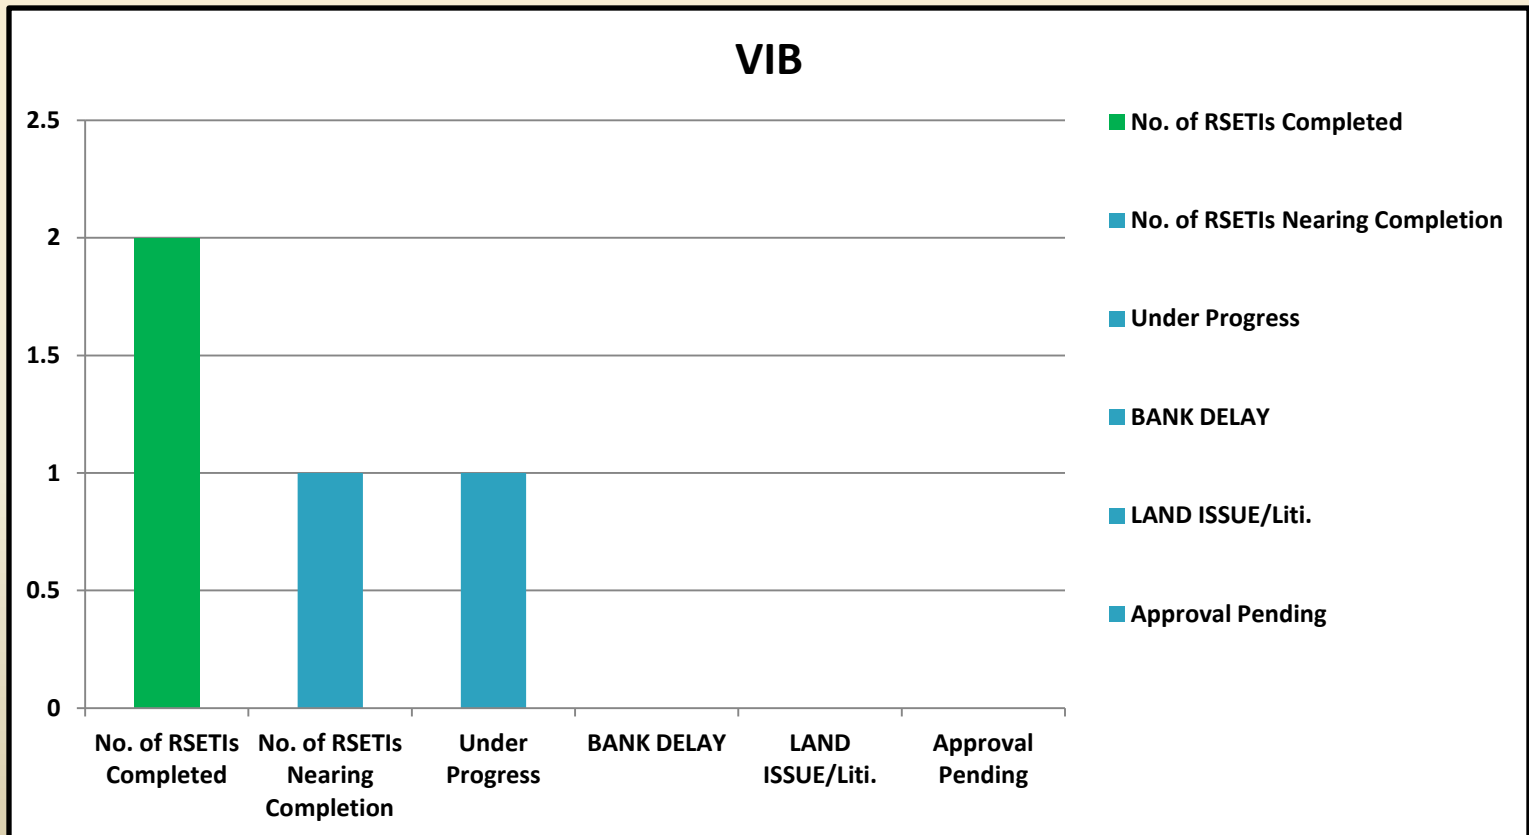


# VIJAYA BANK

<b>S.No</b>	<b>RSETI</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	<b>REMARKS</b>
<b>UNDER PROGRESS</b>				
1	Pasighat***	Arunachal Pradesh	50.00000	LIKELY TO COMPLETE ON 31-12-2017
<b>COMPLETED</b>				
1	Mandya	Karnataka	100.00000	COMPLETED
2	Haveri	Karnataka	100.00000	COMPLETED
<b>NEARING COMPLETION</b>				
1	Indore	Madhya Pradesh	77.83000	LIKELY TO CMPLT ON 30-4-2017

## PUNJAB NATIONAL BANK (PNB) - 53

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
8	16	9	0	16	4

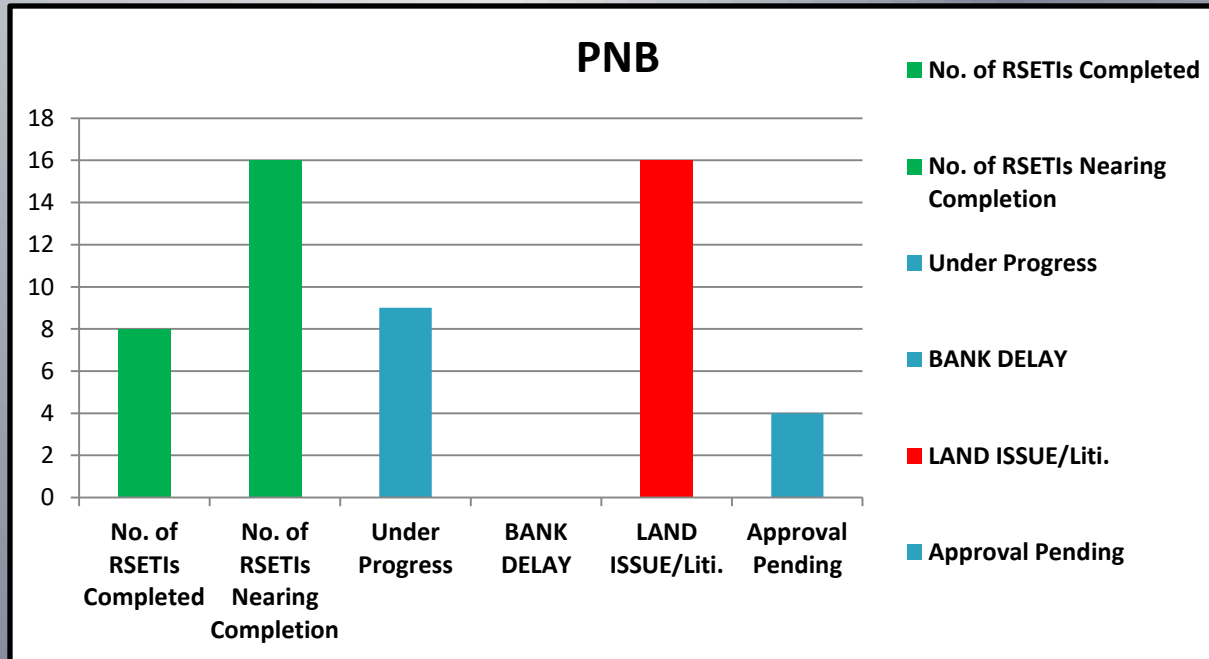

# PUNJAB NATIONAL BANK

S.N	RSETIs	STATE	FUNDS RELEASED	REMARKS
<b>LITIGATIONs/ LAND ISSUEs</b>				
1	Patna	Bihar	50.00000	Land on both side of railway track, Alternate land Identified, MoU EXECUTED SHORTLY, it is <b>pending due to non resolution of land issue and forcing us to drop the proposal of construction of RSETI.</b>
2	Mandi	H.P.	50.00000	<b>LITIGATION</b> - Construction started - 20.8.2015, <b>CONSTRUCTION STOP, DUE TO ISSUE VILLAGERS</b> and falling of allotted area under NHA. Alternate suitable land to be allotted by DA. Construction is pending due to non-resolution of land issue.
3	Jind	Haryana	50.00000	<b>Issue of allotment of alternate</b> suitable land is pending with DA
4	Yamunanagar	Haryana	50.00000	<b>LITIGATION</b> - Construction Started - 6.8.2015 <b>Construction work stop by DTP</b> & Matter has taken up with DM for CLU, Response is still awaited from State Government.
5	Jhajjar	Haryana	50.00000	<b>LITIGATION</b> - Construction Started -6.8.2015 Earlier allotted land belonged to animal husbandry dept. where the DM stopped the construction work recently. DM, has allotted alternate land at village gudda. Now BDO has asked sarpanch to get resolution for providing additional land. <b>Construction is pending due to non-resolution of land issue.</b>
6	Ramgarh Cantt	Jharkhand	50.00000	Construction work allotted to BSNL. The allotted land is on hill lock area. District administration has allotted alternate land recently. Allotted land is not in proper shape and size. <b>Construction is pending due to non-resolution of land issue</b>
7	Hoshiarpur	Punjab	50.00000	Construction Work allotted to HPL & Plan & Estimate RECEIVED AT HO, <b>Administrative Approval pending PNBCRDT HO</b> , Site is pending due to non resolution of Land Issue. According to NH guidelines it is non-viable to construct building.

**PUNJAB NATIONAL BANK**

**Cont.**

<b>S.NO</b>	<b>RSETI</b>	<b>STATE</b>	<b>FUNDs</b>	<b>REMARKS</b>
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Sirsa	Haryana	50.00000	Construction Started - <b>7.8.2015</b>
2	<b>Gurdaspur – NEW ESTB - July 2017</b>	Punjab	50.00000	<b>Alternate land yet to be allotted</b> for construction of RSETI
3	Lakhisarai	Bihar	50.00000	<b>LITIGATION RESOLVED</b> - Construction Started - 11.8.2015, <b>Construction stalled by DM</b> , alternate land allotted by DM, which is less than min requirement of 0.5 acres in terms of MoRD guidelines, requested circle head to provide alternate/additional land
<b>APPROVAL PENDING</b>				
1	Gaya	Bihar	50.00000	<b>LITIGATION RESOLVED</b> - Construction work stalled by DM, <b>Now MoU for alternate land has been done with DDC gaya.</b> Building plan has been submitted by the construction agency. Administrative approval for the same is to be granted by PNBCRDT HO
2	Nawada	Bihar	50.00000	Construction work allotted to BSNL, Bldg Plan and estimates have been submitted by BSNL, <b>Administrative Approval is to be granted by PNBCRDT HO.</b>
3	Kurukshetra	Haryana	50.00000	<b>LITIGATION RESOLVED</b> - Construction work allotted to BSNL, construction work stopped due to CLU now CLU has been obtained. However due to technical observation of DTP, Providing lift or ramp, <b>fresh layout plan submitted by BSNL and waiting for approval.</b>
4	Jhansi	U.P.	50.00000	Construction Allotted to HPL & <b>Map approval Pending from Jhansi Development Authority demanded to pay charges of Rs. 40 lakhs before granting the permission</b>

# PUNJAB NATIONAL BANK

Cont.

S.N	RSETIs	STATE	FUNDS RELEASED	REMARKS
<b>LITIGATIONs/ LAND ISSUEs</b>				
1	Mohali (SAS NGR)	Punjab	50.00000	Alternate land allotted, it is still not clearly in possession of RSETI and MoU for alternate land is executed by the DA, matter is still under litigation and issue is pending in high court, next date of hearing is 28.11.2017 due to on going court case the GP is reluctant to signing up of supplementary lease deed for modification of terms of original lease deed. <b>it is not visible to construct bldg as per MoRD guideline.</b>
2	Dholpur	Rajasthan	50.00000	<b>Construction started - 22.8.2015 Change in Land Use Pending with State Revenue Department.</b> Site is pending due to non resolution of land issue
3	Sikar	Rajasthan	50.00000	Land Use Pending with State Revenue Department. State Govt not rspndg, only 0.5 acre of land allotted 12.8.2015, allotted land pending with Urban Improvement Trust (UIT), <b>Non resolution of land issue</b>
4	Badaun	U.P.	50.00000	Alternate land allotted & contract given to HPL, revised estimate given by HPL, <b>Site is pending due to non resolution of land issue</b> (NH)
5	Bulandshahr	U.P.	50.00000	Alternate Land yet to be allotted, we are following up the matter for last 2 years, site is pending due to non resolution of land issue.
6	Lalitpur	U.P.	50.00000	<b>Litigation: Construction work has been stopped.</b> Construction site has been blocked , matter has been taken up with DA.

# PUNJAB NATIONAL BANK

**Cont.**

S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	Arwal	Bihar	50.00000	Likely to be completed on <b>30.6.2018</b>
2	Aurangabad	Bihar	89.94000	Likely to be completed on <b>30.6.2018</b>
3	Arrah (Bhojpur)	Bihar	85.67000	Likely to be completed on <b>30.6.2018</b>
4	Buxar	Bihar	50.00000	Likely to be completed on <b>30.6.2018</b>
5	Jehanabad	Bihar	50.00000	Third tender has been finalized, Constrn Started - 12.8.2015 <b>Under Progress</b>
6	Rohtas (Sasaram)	Bihar	50.00000	CNSTRN UNDER PROGRESS - <b>30.6.2018</b>
7	Hamirpur	H.P.	100.00000	CNSTRN UNDER PROGRESS - <b>30.6.2018</b>
8	Kangra	H.P.	50.00000	CNSTRN UNDER PROGRESS - <b>30.6.2018</b>
9	Saraikela Kharsawan	Jharkhand	86.33000	Likely to be completed on <b>30.6.2018</b>
<b>COMPLETED</b>				
1	Kaithal	Haryana	100.00000	<b>COMPLETED</b>
2	Panipat	Haryana	50.00000	<b>COMPLETED</b>
3	Narnaul	Haryana	90.05000	<b>COMPLETED</b>
4	Rewari	Haryana	90.06000	<b>COMPLETED</b>
5	Panchkula	Haryana	100.00000	<b>COMPLETED</b>
6	Jhalarapatan	Rajasthan	100.00000	<b>COMPLETED</b>
7	Muzaffarnagar	U.P.	100.00000	<b>COMPLETED</b>
8	Saharanpur	U.P.	100.00000	<b>COMPLETED</b>


**PUNJAB NATIONAL BANK****Cont.**

<b>S.NO</b>	<b>RSETIs</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	<b>REMARKS</b>
<b>NEARING COMPELTION</b>				
1	Bhabua (Kaimur)	Bihar	84.48000	Likely to be completed on <b>31.3.2018</b>
2	Nalanda	Bihar	85.85000	Likely to be completed on <b>31.3.2018</b>
3	Kullu	H.P.	100.00000	NEARING COMPLETED- <b>31.12.2017</b>
4	Una	H.P.	100.00000	Likely to be completed on <b>31.3.2018</b>
5	Ambala	Haryana	100.00000	NEARING COMPLETED - <b>31.3.2018</b>
6	Bhiwani	Haryana	89.98000	NEARING COMPLETED
7	Hisar	Haryana	86.98000	NEARING COMPLETED
8	Karnal	Haryana	50.00000	NEARING COMPLETED
9	Rohtak	Haryana	100.00000	NEARING COMPLETED
10	Sonepat	Haryana	100.00000	NEARING COMPLETED - <b>31.12.2017</b>
11	Datia	Madhya Pradesh	88.62000	Likely to be completed on <b>31.3.2018</b>
12	East Khasi Hills	Meghalaya	98.73000	Likely to be completed on <b>31.3.2018</b>
13	Amritsar	Punjab	100.00000	Likely to be completed on <b>31.3.2018</b>
14	Kapurthala	Punjab	100.00000	NEARING COMPLETED- <b>31.3.2018</b>
15	Bijnor	U.P.	100.00000	Likely to be completed on <b>31.3.2018</b>
16	Haridwar	Uttarakhand	100.00000	Likely to be completed on <b>31.3.2018</b>



## RUDSETI - 24

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>17</b>	<b>3</b>	<b>0</b>	<b>4</b>	<b>1*</b>	<b>0</b>

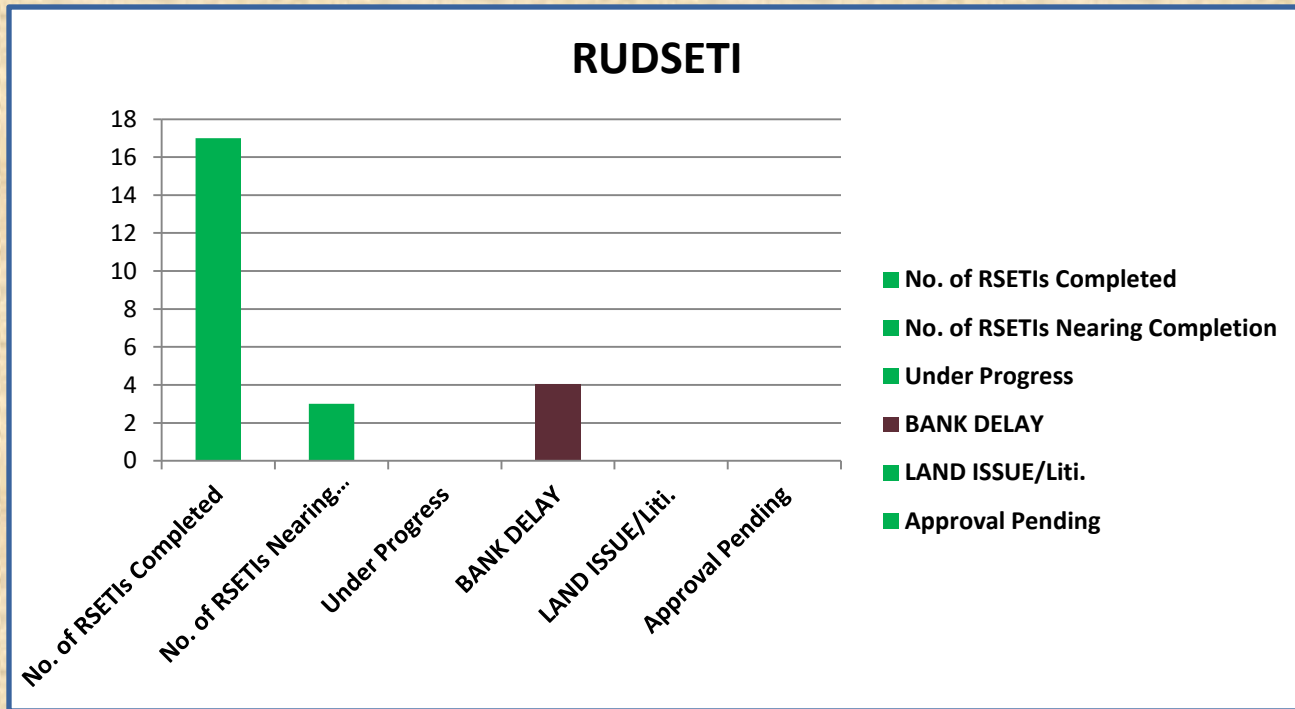


## RUDSETI

S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Nagaon	Assam	50.00000	Land Allotted on 17.11.2017, <b>Action initiated for Construction</b>
2	Hajipur, Vashali,	Bihar	50.00000	Floated of tender is estimated to be implemented.. <b>Construction work is estimate to start shortly</b>
3	Madurai	Tamilnadu	50.00000	<b>Contractor</b> yet to be appointed
4	Agartala	Tripura	50.00000	MoU Signed, Soil test may be done by agarthala muncipal corp. <b>Approved of bldg plan.</b>
<b>NEARING COMPLETION</b>				
1	Gurgaon	Haryana	99.69048	<b>Wood work</b> is going on
2	Ranchi	Jharkhand	50.00000	Likely to be completed by <b>march 2018</b>
3	Bhopal	Madhya Pradesh	99.01089	Likely to be completed by <b>march 2018</b>
<b>LAND ISSUEs</b>				
1	Jalandhar	Punjab	10.00000	The land which is allotted is <b>disputed land.</b> 4.1.2018 meeting GP

<b>RUDSETI</b>				<b>Cont.</b>
<b>S.No</b>	<b>RSETI</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	
<b>COMPLETED</b>				
1	Ongole, Prakasham	Andhra Pradesh	100.00000	
2	Bijapur/Vijaypura	Karnataka	93.45000	
3	Chitradurga	Karnataka	100.00000	
4	Dharwad	Karnataka	94.57000	
5	Ujire	Karnataka	90.98000	
6	Mysore	Karnataka	99.58000	
7	Brahmavar, Udupi	Karnataka	90.93000	
8	Bhilwara	Rajasthan	100.00000	
9	Baran	Rajasthan	100.00000	
10	Berhampore, Mushirabad	West Bengal	100.00000	

## SYNDICATE BANK - 14

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
2	1	1	6	2	2

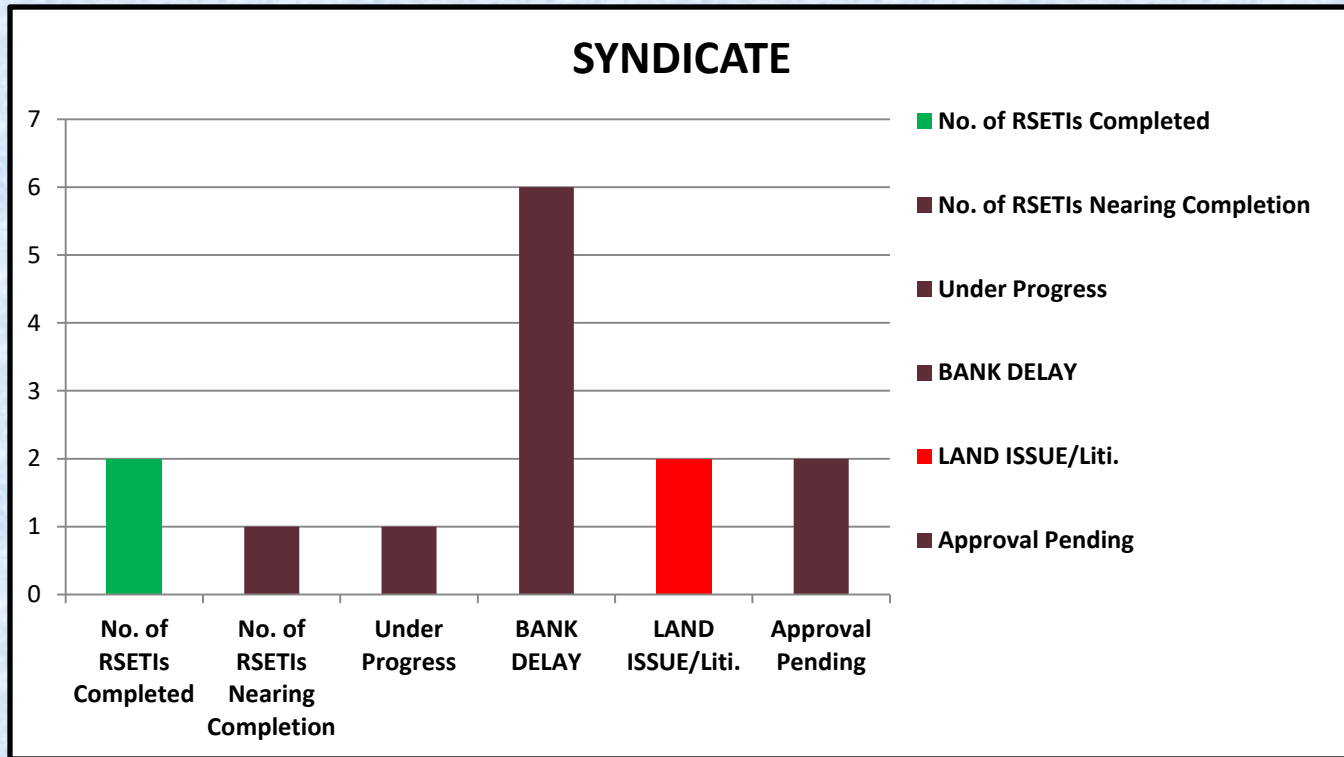

## SYNDICATE BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Kurnool	Andhra Pradesh	50.00000	Earlier allotted land is unsuitable for construction, <b>Alternate land yet to be allotted</b>
2	Faridabad	Haryana	50.00000	Request to Dist. Administration for <b>allotment of alternate land</b>
<b>APPROVAL PENDING</b>				
1	Meerut	U.P.	60.00000	Plan Approved & <b>estimate being prepared</b>
2	GN Nagar, Noida	U.P.	50.00000	Estimate Approval <b>under progress</b>
<b>UNDER PROGRESS</b>				
1	Mewat	Haryana	50.00000	Construction started, foundation completed 8500 SQ. FTS. <b>Redrawn to reduce the area of construction.</b>
<b>NEARING COMPLETION</b>				
1	Belgaum	Karnataka	100.00000	Finishing stage- <b>contractor withdraw</b> from the project, we are in the process of <b>appointing another contractor.</b>


## SYNDICATE BANK

**Cont.**

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>COMPLETED</b>				
1	Kadapa	Andhra Pradesh	80.37000	Inauguration planned before <b>31.1.2018</b>
2	Kumta	Karnataka	100.00000	<b>COMPLETED</b>
<b>BANK DELAY</b>				
1	Bellary	Karnataka	50.00000	<b>Plan preparation</b> is under progress
2	Kollam	Kerala	50.00000	<b>Appointment of Architect</b> being done
3	Kavaratti	Lakshadweep	50.00000	Land for construction is very less, requested to MoRD to relx the min area of construction. MoRD has released the min area of construction. <b>The process will be initiated shortly</b>
4	Mathura	U.P.	50.00000	MVDA demanding of <b>Rs. 30.25 LAKH</b> as development and conversion charges.
5	Moradabad	U.P.	50.00000	Architect appointed recently, <b>preparation of plan</b> is under progress
6	J.P.Nagar Amroha	U.P.	50.00000	Appointment of <b>Architect</b> being done

## UNITED BANK OF INDIA - 5

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>1</b>	<b>0</b>	<b>0</b>	<b>4</b>	<b>0</b>	<b>0</b>

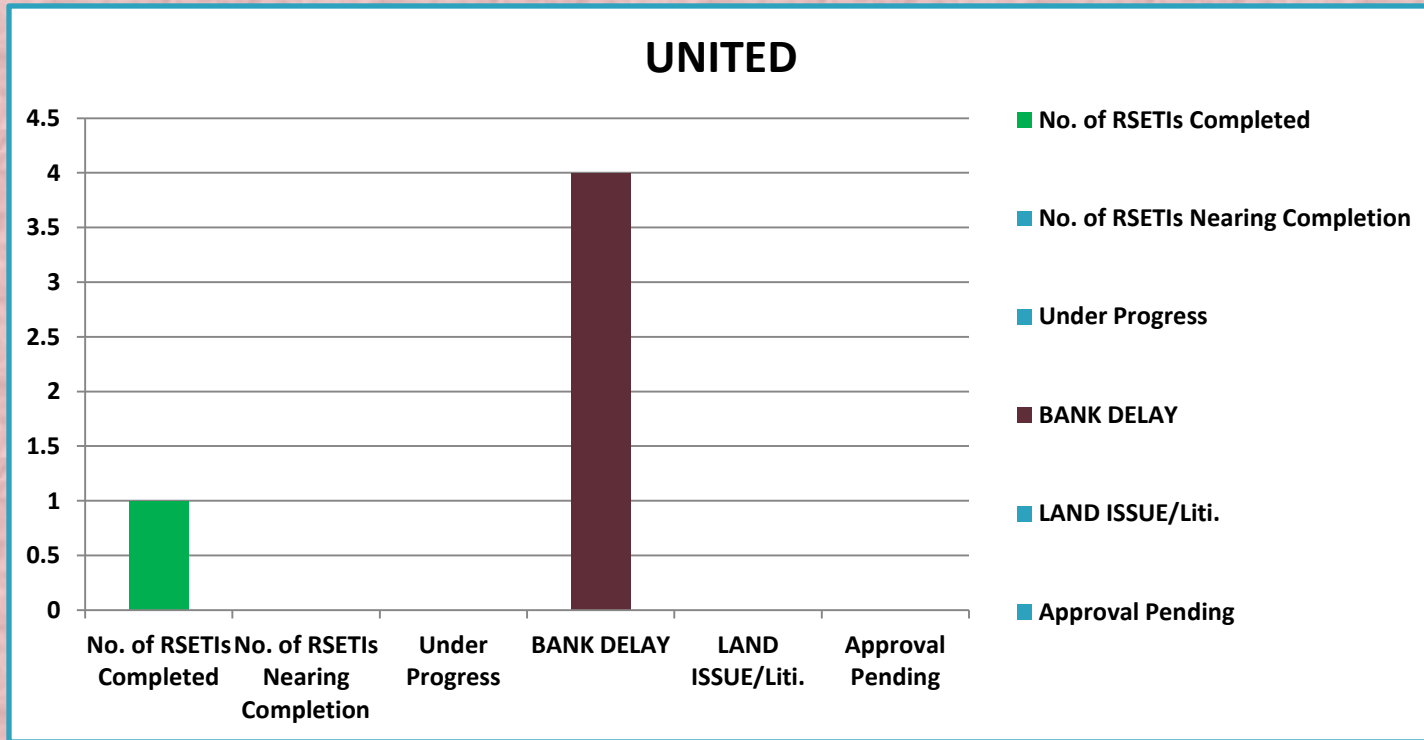



# UNITED BANK OF INDIA


S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Dhemaji	Assam	50.00000	Initial effort to select construction firm failed(BSNL), <b>Process started to select construction firm afresh</b>
2	Lakhimpur	Assam	50.00000	Initial effort to select construction firm failed(BSNL), <b>Process started to select construction firm afresh</b>
3	Dhalai	Tripura	50.00000	Initial effort to select construction firm failed(BSNL), <b>Process started to select construction firm afresh</b>
4	South Tripura	Tripura	50.00000	Initial effort to select construction firm failed(BSNL), <b>Process started to select construction firm afresh</b>
<b>OWN BUILDING – MODIFICATION UNDER PROGRESS</b>				
1	South Parganas	West Bengal	50.00000	<b>Bank has taken initiative for Upgrading the Modifications for Existing building</b>



## UNION BANK - 14

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>7</b>	<b>1</b>	<b>1</b>	<b>2</b>	<b>2</b>	<b>1</b>

### UNION

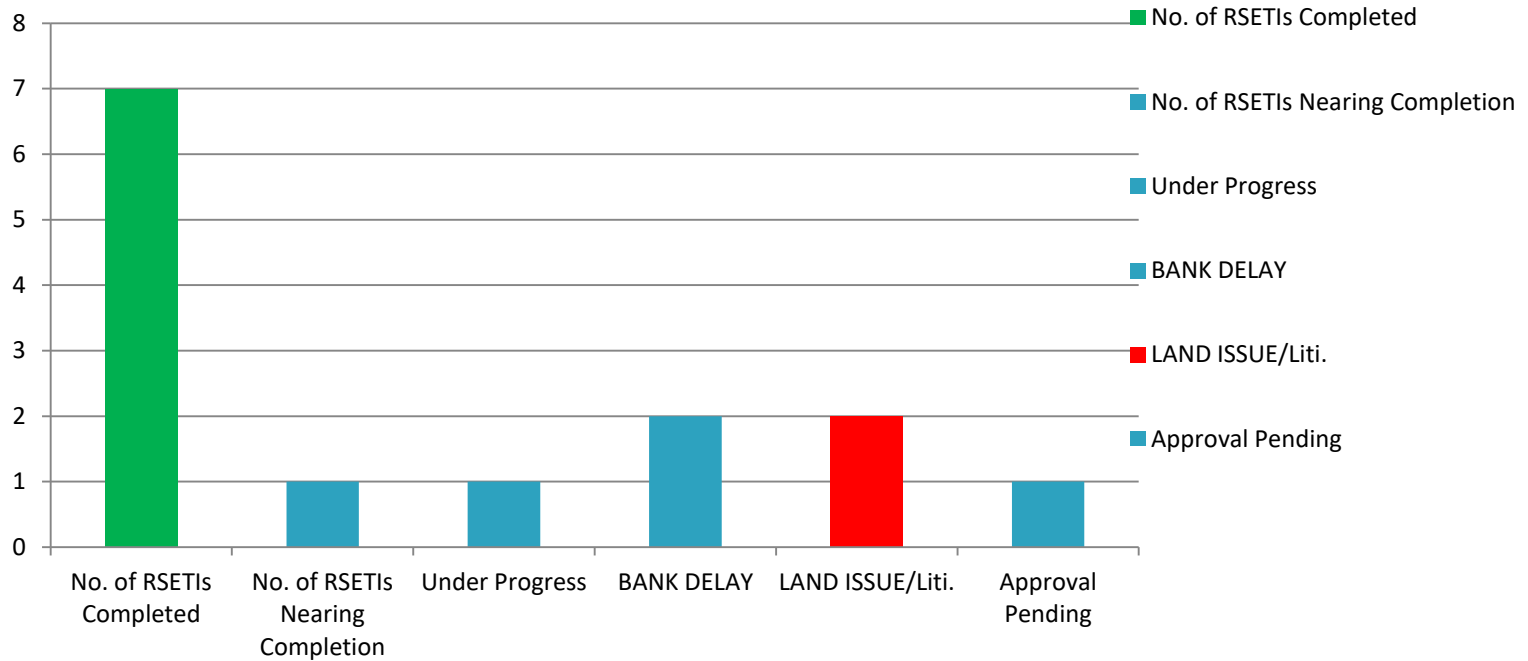

# UNION BANK OF INDIA


S.NO	RSETIs	STATE	FUNDS RELEASED	REMARKS
<b>LAND ISSUES</b>				
1	Khagaria,	Bihar	50.00000	The previous allotted site was of 1 acre but available site is only half acre and local administration has constructed some bldgs in allotted area. Local Admin has allotted 0.511 arce land. Project architect has visited the site and <b>preparing revised plans for construction.</b>
2	Idukki	Kerala	50.00000	Work order issued to the contractor, Local authority objecting for construction on allotted land. local authority is denying providing the same land. It is informed that the govt. has identified a suitable land near nedumkadam and <b>commissioner RD is going to submit a report to govt. shortly.</b>
<b>APPROVAL PENDING</b>				
1	Samastipur	Bihar	50.00000	Allotted land is to be demarcated afresh by the local authority and the site has to be cleared for layout of actual execution of work. The area is flood prone, <b>project architect has prepared estimate and construction work to start soon</b>
<b>UNDER PROGRESS</b>				
1	Rewari	Madhya Pradesh	50.00000	Civil construction work is <b>in progress may -18</b>
<b>BANK DELAY</b>				
1	Azamgard	U.P.	50.00000	Contractor appointed and <b>construction work will start soon</b>
2	Chandauli	U.P.	50.00000	Word order to the appointed contractor issued, <b>construction work start soon</b>
<b>NEARING COMPLETION</b>				
1	Santravidas nagar	U.P.	50.00000	<b>70% work is completed</b>

**UNION BANK OF INDIA****Cont.**

<b>S.No</b>	<b>RSETIs</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	<b>REMARKS</b>
<b>COMPLETED</b>				
1	Erranakulam	Kerala	100.00000	<b>COMPLETED</b> -Civil construction work is completed
2	Sidhi	Madhya Pradesh	50.00000	<b>COMPLETED</b> -Civil construction work is completed
3	Singrauli	Madhya Pradesh	50.00000	<b>COMPLETED</b> -Civil construction work is completed
4	Ghazipur	U.P.	50.00000	<b>COMPLETED</b>
5	Jaunpur	U.P.	100.00000	<b>CONSTRN WORK CMLPTD</b>
6	Mau	U.P.	100.00000	<b>CONSTRN WORK CMLPTD</b>
7	Varanasi	U.P.	100.00000	<b>CONSTRN WORK CMLPTD</b>

## UCO BANK - 21

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>2</b>	<b>2</b>	<b>7</b>	<b>7</b>	<b>2</b>	<b>1</b>

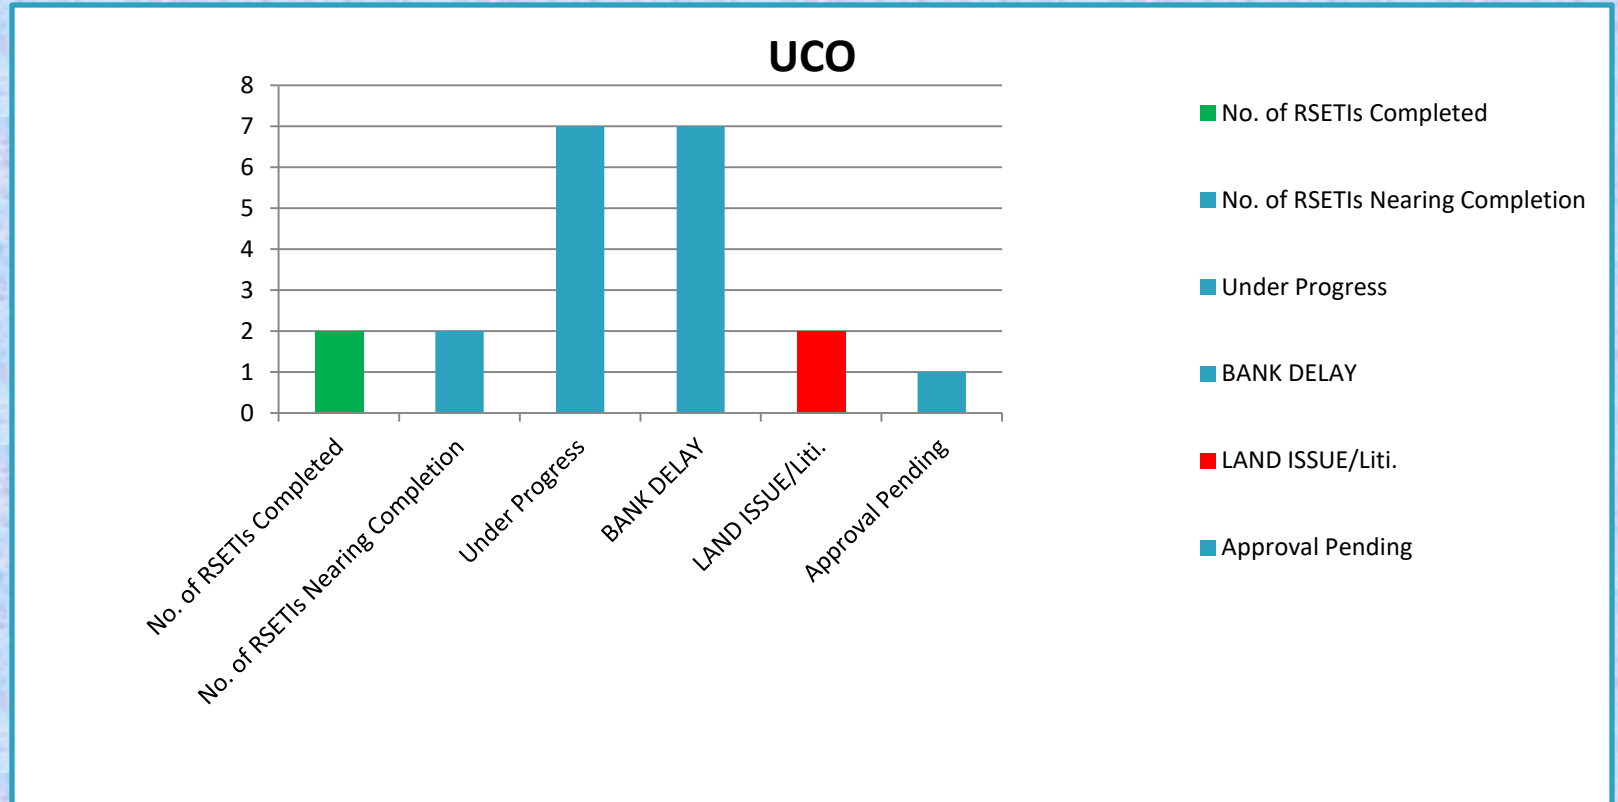

# UCO BANK

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>LAND ISSUE</b>				
1	Barpeta	Assam	50.00000	LAND IS VIRTUALLY A POND/LOW LAND, <b>LOOKING FOR ALTR LAND</b>
<b>POSSESSION YET TO BE TAKEN</b>				
1	Puri**	Orissa	10.00000	Collector instructed to deposit 88000 for annual gross and Rs. 66000 for cess. <b>RSETI to deposit the amount</b>
2	Burdwan	West Bengal	50.00000	Initial land allotted, state govt. project was build upon the allotted plot. <b>The district authority is looking for another suitable plot</b>
<b>BANK DELAY</b>				
1	Darrang	Assam	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.38 Crores.</b>
2	Dhubri	Assam	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.38 Crores.</b>
3	Kokrajhar	Assam	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.46 Crores.</b>
4	Nalbari	Assam	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.45 Crores.</b>
5	Banka	Bihar	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.32 Crores.</b>
6	Bhagalpur	Bihar	50.00000	Tender has been floated and work order has been issued. <b>Budget estimated at Rs. 1.36 Crores.</b>
7	Rupnagar	Punjab	50.00000	Estimate <b>approval pending</b>


## UCO BANK

Cont.

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>COMPLETED</b>				
1	Balasore	Orissa	100.00000	Inaugurated on 20.12.2016
2	Begusarai	Bihar	100.00000	Functioning in its own bldg since 1.3.2016 hostel facility started on 10.7.2017
<b>APPROVAL PENDING</b>				
1	Monghyr	Bihar	50.00000	Revised Plan & Estimate approval is pending
<b>UNDER PROGRESS</b>				
1	Bilaspur	H.P.	50.00000	Construction started Budget estimate at Rs. 1.64 Crores
2	Goalpara	Assam	50.00000	Likely to complete in august -18
3	Shimla	H.P.	50.00000	Work order has been issued and construction started budget estimate at Rs. 1.50 Crores.
4	Sirmaur	H.P.	50.00000	Work order has been issued and construction started budget estimate at Rs. 1.48 Crores.
5	Solan	H.P.	50.00000	Work order has been issued and construction started budget estimate at Rs. 1.87 Crores.
6	Dausa	Rajasthan	50.00000	Likely to complete on Feb-18
7	Nagaur	Rajasthan	50.00000	Likely to complete on JAN 2018
<b>NEARING COMPLETION</b>				
1	Bhadrak	Orissa	100.00000	Electric connection is submitted to electricity department and after getting connection RSETI shifted to New bldg
2	Jagatsingpur	Orissa	50.00000	Likely to be complete on Dec-17

## STATE BANK OF INDIA (SBI) - 132

No. of RSETIs Completed	No. of RSETIs Nearing Completion	Under Progress	BANK DELAY	LAND ISSUE/Liti.	Approval Pending
<b>63</b>	<b>19</b>	<b>21</b>	<b>7</b>	<b>10</b>	<b>12</b>

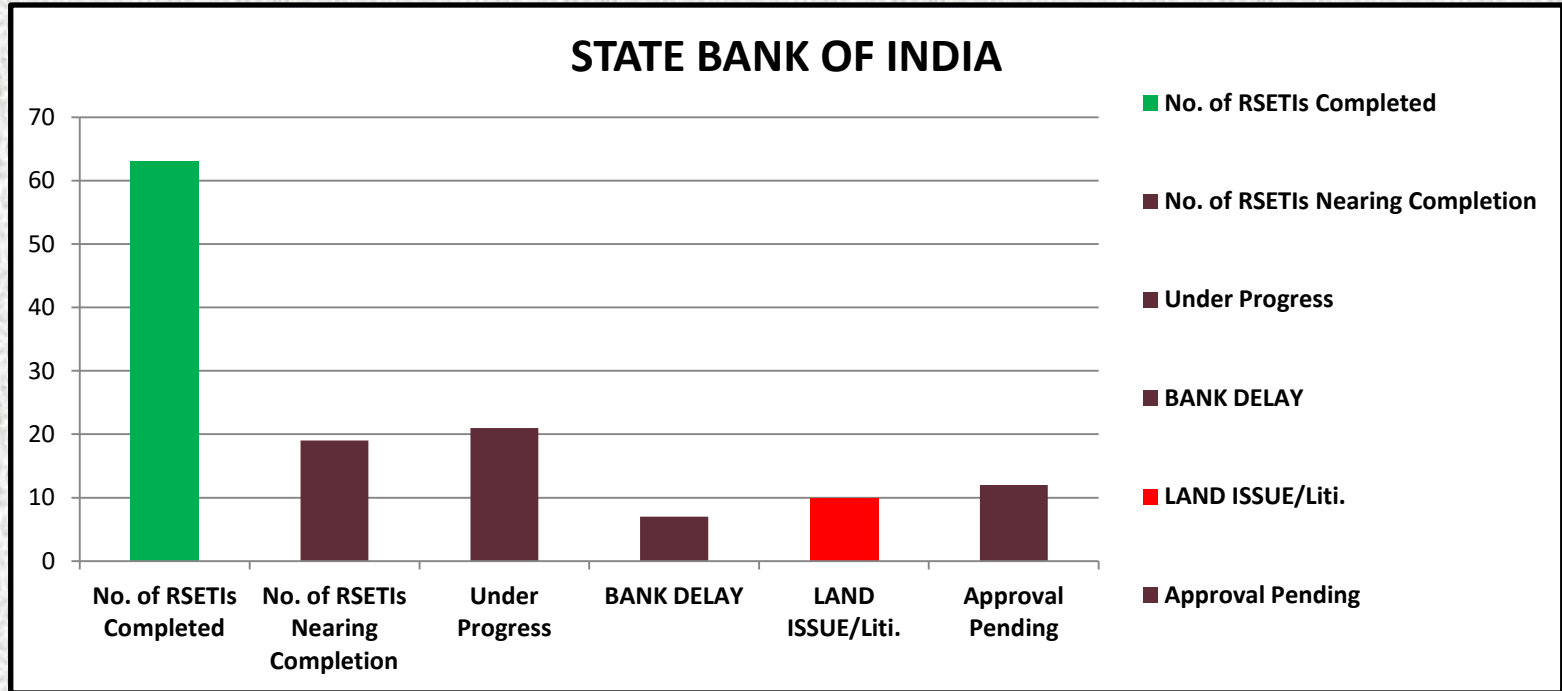



## LHO AMARAVATHI

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>LAND ISSUE</b>				
1	Visakhapatnam,	Andhra Pradesh	50.00000	LAND ALLTD, BUT <b>DEMARCATON/SURVEY SITE PENDING WITH STATE GOVT.</b>

## LHO BHOPAL

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Jashpurnagar	Chhattisgarh	50.00000	Likely to be complete <b>Mar 2018</b>

## LHO JAIPUR

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	Bikaner	Rajasthan	100.00000	<b>Construction stopped</b> by the contractor likely to be completed on 30.6.2018
<b>LAND ISSUE</b>				
1	Jalore	Rajasthan	50.00000	<b>Court Case by third party</b> to cancel allotment of land in favor of RSETI Jalore
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Pali	Rajasthan	50.00000	<b>Matter Pending</b> with State level



## LHO PATNA

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Jamui,	Bihar	96.69000	Construction work is in final stage - <b>Jan - 2018</b>
2	Saharsa	Bihar	96.27000	Finishing Stage <b>March-18</b>
<b>LITIGATION</b>				
1	Supaul	Bihar	50.00000	LITIGATION LIKE TO BE RESOLVED BY <b>Nov 2017</b>
<b>UNDER PROGRESS</b>				
1	Garhwa	Jharkhand	50.00000	<b>SEPT 2018</b> LIKE TO BE COMPLETE
2	Jamtara	Jharkhand	50.00000	<b>SEPT 2018</b> LIKE TO BE COMPLETE
3	Latehar	Jharkhand	50.00000	<b>SEPT 2018</b> LIKE TO BE COMPLETE
4	Pakur	Jharkhand	50.00000	Likely to be complete on <b>Dec-18</b>
5	Palamu (Daltonganj)	Jharkhand	50.00000	Likely to be complete on <b>OCT-18</b>
6	Madhepura	Bihar	50.00000	<b>Sept 2018</b> LIKE TO BE COMPLETE
7	Sahibganj	Jharkhand	50.00000	<b>Jun-18</b>
8	Araria,	Bihar	50.00000	Likely to be complete on <b>March-2019</b>

## LHO CHENNAI

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Tuticorin/Thoothukudi,	Tamilnadu	50.00000	<b>NEARING COMPLETION</b>

## LHO AHMEDABAD

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	Surendranagar	Gujarat	50.00000	Construction work was started. Construction work was started on April 2017, <b>Likely to be completed on 31.7.2018</b>
<b>LAND YET TO BE ALLOTTED</b>				
2	Bhavnagar	Gujarat	10.00000	Building is provided by the state govt. <b>Matter is pending with Collectrate</b>

## LHO CHANDIGARH

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Fatehabad	Haryana	50.00000	Plan Approved, <b>Construction not yet started</b>
2	Ladakh (Leh)	J & K	50.00000	Possession Given, <b>Construction not yet started</b>
<b>UNDER PROGRESS</b>				
1	Fatehgarh Sahib	Punjab	50.00000	likely to be complete <b>30.6.2018</b>
2	Mansa	Punjab	50.00000	likely to be complete <b>30.6.2018</b>
3	Barnala	Punjab	50.00000	likely to be complete <b>30.6.2018</b>
4	Mukatsar	Punjab	50.00000	likely to be complete <b>30.6.2018</b>
<b>APPROVAL PENDING</b>				
1	Bathinda	Punjab	50.00000	<b>Plan Approval Pending</b>

## LHO BANGALURU

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	BITSERD, Yadgir	Karnataka	50.00000	Construction work of <b>ground floor slab</b> is completed
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
2	Koppal	Karnataka	49.60000	<b>Alternate land yet to be allotted</b>

## LHO TRAVANCORE

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>BANK DELAY</b>				
1	Alappuzha	Kerala	50.00000	Land Dispute case resolved recently - <b>construction initiate soon</b>
2	Kottayam,	Kerala	50.00000	<b>Plan &amp; Estimate to be prepared</b>
3	Wayanad,	Kerala	50.00000	Land allotted in block panchayat and the bank is proceeding with the <b>steps for construction</b>
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Pathanamthitta,	Kerala	50.00000	Allotted land with building given to another govt. depart. As per high court verdict. Dispute Case-Land - <b>Alternate land yet to allotted</b>

**LHO BHOPAL**

<b>S.No</b>	<b>RSETIs</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	<b>REMARKS</b>
<b>NEARING COMPLETION</b>				
1	Harda	Madhya Pradesh	80.74000	Likely to be completed <b>march 2018</b>
<b>BANK DELAY</b>				
2	Neemuch	Madhya Pradesh	50.00000	Land allotted by dist. Authority on 3.12.2017 <b>Possession has been given</b>
<b>APPROVAL PENDING</b>				
3	Umaria	Madhya Pradesh	50.00000	Plan Approval Pending with <b>T&amp;CP Dept.</b>
<b>UNDER PROGRESS</b>				
4	Vidisha	Madhya Pradesh	50.00000	Construction <b>Under Progress</b> - 31.6.2018

**LHO MUMBAI**

<b>S.No</b>	<b>RSETIs</b>	<b>STATE</b>	<b>FUNDS RELEASED</b>	<b>REMARKS</b>
<b>APPROVAL PENDING</b>				
1	Nanded	Maharashtra	50.00000	<b>Plan approval pending</b> with Dist. Authority
2	Beed	Maharashtra	50.00000	<b>Plan Approval &amp; Estimate is under process</b>
<b>BANK DELAY</b>				
1	Nandurbar	Maharashtra	50.00000	<b>Cost estimates Rs. 2.50 crore.</b> Arrangements for difference of funds from corporate centre is sought for.

# LHO GUWAHATI

S.No	RSETIs	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Churachandpur	Manipur	94.04000	LIKELY TO COMPLETE ON <b>March 2018</b>
2	Peren cluster	Nagaland	50.00000	LIKELY TO COMPLETE ON <b>March 2018</b>
3	Udalgiri	Assam	84.14000	LIKE TO INAUGURATED BY <b>JAN 2018</b>
4	Ribhoi/Umran	Meghalaya	50.00000	LIKELY TO COMPLETE ON <b>Feb 2018</b>
<b>APPROVAL PENDING</b>				
1	Aizawl Cluster (Aizawl, Mamit, Serchip, Champhai)	Mizoram	50.00000	<b>Delay for land problem</b> , possessed after 3 times change. Applied for CSR fund <b>(Ministry Question reg.. 8.3.2018)</b>
2	West Garo Hills (West & South Garo Hills)	Meghalaya	50.00000	Estimate wanted by Local authority along with labour ches of Rs. 88444/ & Building fee of Rs. 44,410/- , <b>Matter taken up with local authority</b>
3	Karbi Anglong	Assam	50.00000	<b>Estimate approval</b> under progress
4	North Cachar Hills	Assam	50.00000	<b>Estimate approval</b> under progress
5	Baksa	Assam	50.00000	Delay for <b>LAND DISPUTE</b> , Applied for CSR Funds
<b>UNDER PROGRESS</b>				
1	Unakoti/North Tripura	Tripura	50.00000	Under progress - Applied for <b>CSR funds</b>



## LHO BHUBANESHWAR

S.NO	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	Bargarh,	Orissa	77.75000	Likely to be completed on <b>march 2018</b>
2	Kalahandi	Orissa	80.52000	Likely to be completed on <b>march 2018</b>
3	Kandhamal	Orissa	87.96000	Likely to be completed on <b>march 2018</b>
4	Koraput	Orissa	78.51000	Likely to be completed on <b>march 2018</b>
5	Malkangiri	Orissa	86.19000	Likely to be completed on <b>march 2018</b>
6	Nuapada	Orissa	81.47000	Likely to be completed on <b>march 2018</b>
7	Rayagada	Orissa	50.00000	Likely to be completed on <b>march 2018</b>
8	Sonepur/Subarnapur	Orissa	77.30000	likely to be completed on <b>feb 2018</b>
<b>UNDER PROGRESS</b>				
1	Sundargarh	Orissa	50.00000	Likely to be completed on <b>Jun-18</b>

## LHO KOLKATA

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>NEARING COMPLETION</b>				
1	SIKKIM EAST CLUSTER - Gangtok	Sikkim	50.00000	LIKELY TO COMPLETE on <b>Mar-18</b>

## LHO TELANGANA

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>LAND ISSUEs</b>				
1	Mahaboobnagar	Telangana	50.00000	Construction @ initial stage , Bhoomi Pooja done
1	Khammam,	Telangana	50.00000	<b>Alternate Land yet to be allotted</b> - Under process

## LHO LUCKNOW

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>UNDER PROGRESS</b>				
1	<b>Basti</b>	U.P.	50.00000	Started JUNE 2017 and Likely to be complete on <b>August 2018</b>
2	<b>Maharajganj,</b>	U.P.	50.00000	Stared July 2017 & Likely to be completed <b>Oct 2018</b>

## LHO DELHI

S.No	RSETI	STATE	FUNDS RELEASED	REMARKS
<b>APPROVAL PENDING</b>				
1	Chamoli (Gopeshwar)	Uttarakhand	50.00000	Sanction for additional fund not received from CSR, <b>work has not been awarded</b> likely to be complete on 30.6.2018
2	Uttarkashi	Uttarakhand	50.00000	Grant received in <b>Jan – 2017, Map plan is pending</b> and construction work start soon.
3	Champawat	Uttarakhand	50.00000	Estimate received on 17.10.2017
<b>UNDER PROGRESS</b>				
1	PauriGarwal (UttarKanshi)	Uttarakhand	50.00000	Civil work on completion stage, we are going to float tenders for furnishing work soon
<b>ALTERNATE LAND YET TO BE ALLOTTED</b>				
1	Rudraprayag	Uttarakhand	50.00000	<b>LAND ISSUE</b> - Identify for New Piece of land is under process
2	Tehri-Garhwal (New Tehri)	Uttarakhand	50.00000	<b>LAND ISSUE</b> - Identify for New Piece of land is under process



Thank You
